ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors
1		**Installation of 200 M3/hr DMRO Chain at HMD**	**298.63 days**	**26 Dec '23**	**14 Feb '25**	
2		Receipt of LOI/Notice to proceed	1 day	26 Dec '23	26 Dec '23	
3		Order Transfer Meeting (Thermax Internal)	1 day	27 Dec '23	27 Dec '23	2
4		Receipt of PO	7 days	27 Dec '23	04 Jan '24	2
5		Kick-Off Meeting (At Site)	2 days	24 Jan '24	25 Jan '24	2FS+20 days
6		**Engineering & Procurement**	**252.88 days**	**26 Dec '23**	**12 Dec '24**	
7		**Process Engineering**	**59 days**	**11 Jan '24**	**02 Apr '24**	
8		**PFD & Mass Balance**	**32 days**	**11 Jan '24**	**23 Feb '24**	
9		Submission	10 days	11 Jan '24	24 Jan '24	3FS+10 days
10		Receipt of 1st comments	12 days	25 Jan '24	09 Feb '24	9
11		Re-submission	5 days	12 Feb '24	16 Feb '24	10
12		Final Approval	5 days	19 Feb '24	23 Feb '24	11
13		**P & I D**	**32 days**	**11 Jan '24**	**23 Feb '24**	
14		Submission	10 days	11 Jan '24	24 Jan '24	3FS+10 days
15		Receipt of 1st comments	12 days	25 Jan '24	09 Feb '24	14
16		Re-submission	5 days	12 Feb '24	16 Feb '24	15
17		Final Approval	5 days	19 Feb '24	23 Feb '24	16
18		**Process Design Basis & Sizing Calculations**	**32 days**	**11 Jan '24**	**23 Feb '24**	
19		Submission	10 days	11 Jan '24	24 Jan '24	3FS+10 days
20		Receipt of 1st comments	12 days	25 Jan '24	09 Feb '24	19
21		Re-submission	5 days	12 Feb '24	16 Feb '24	20
22		Final Approval	5 days	19 Feb '24	23 Feb '24	21
23		**Other Process Documents**	**32 days**	**19 Feb '24**	**02 Apr '24**	
24		Submission	10 days	19 Feb '24	01 Mar '24	16,21
25		Receipt of 1st comments	12 days	04 Mar '24	19 Mar '24	24
26		Re-submission	5 days	20 Mar '24	26 Mar '24	25
27		Final Approval	5 days	27 Mar '24	02 Apr '24	26
28		**HAZOP**	**16 days**	**26 Feb '24**	**18 Mar '24**	
29		Conductance	1 day	26 Feb '24	26 Feb '24	17,22
30		Release of HAZOP Report	5 days	27 Feb '24	04 Mar '24	29
31		Closure of HAZOP Report	10 days	05 Mar '24	18 Mar '24	30
32		**Projects Documentation**	**69 days**	**26 Jan '24**	**01 May '24**	
33		**Vendor List**	**22 days**	**26 Jan '24**	**26 Feb '24**	
34		Submission	5 days	26 Jan '24	01 Feb '24	5
35		Receipt of 1st comments	7 days	02 Feb '24	12 Feb '24	34
36		Re-submission	5 days	13 Feb '24	19 Feb '24	35
37		Final Approval	5 days	20 Feb '24	26 Feb '24	36
38		**Billing Break-up For Supply**	**24 days**	**26 Feb '24**	**28 Mar '24**	
39		Submission	7 days	26 Feb '24	05 Mar '24	17,22
40		Receipt of 1st comments	7 days	06 Mar '24	14 Mar '24	39
41		Re-submission	5 days	15 Mar '24	21 Mar '24	40
42		Final Approval	5 days	22 Mar '24	28 Mar '24	41
43		**Billing Break-up For E & C**	**24 days**	**29 Mar '24**	**01 May '24**	
44		Submission	7 days	29 Mar '24	08 Apr '24	42

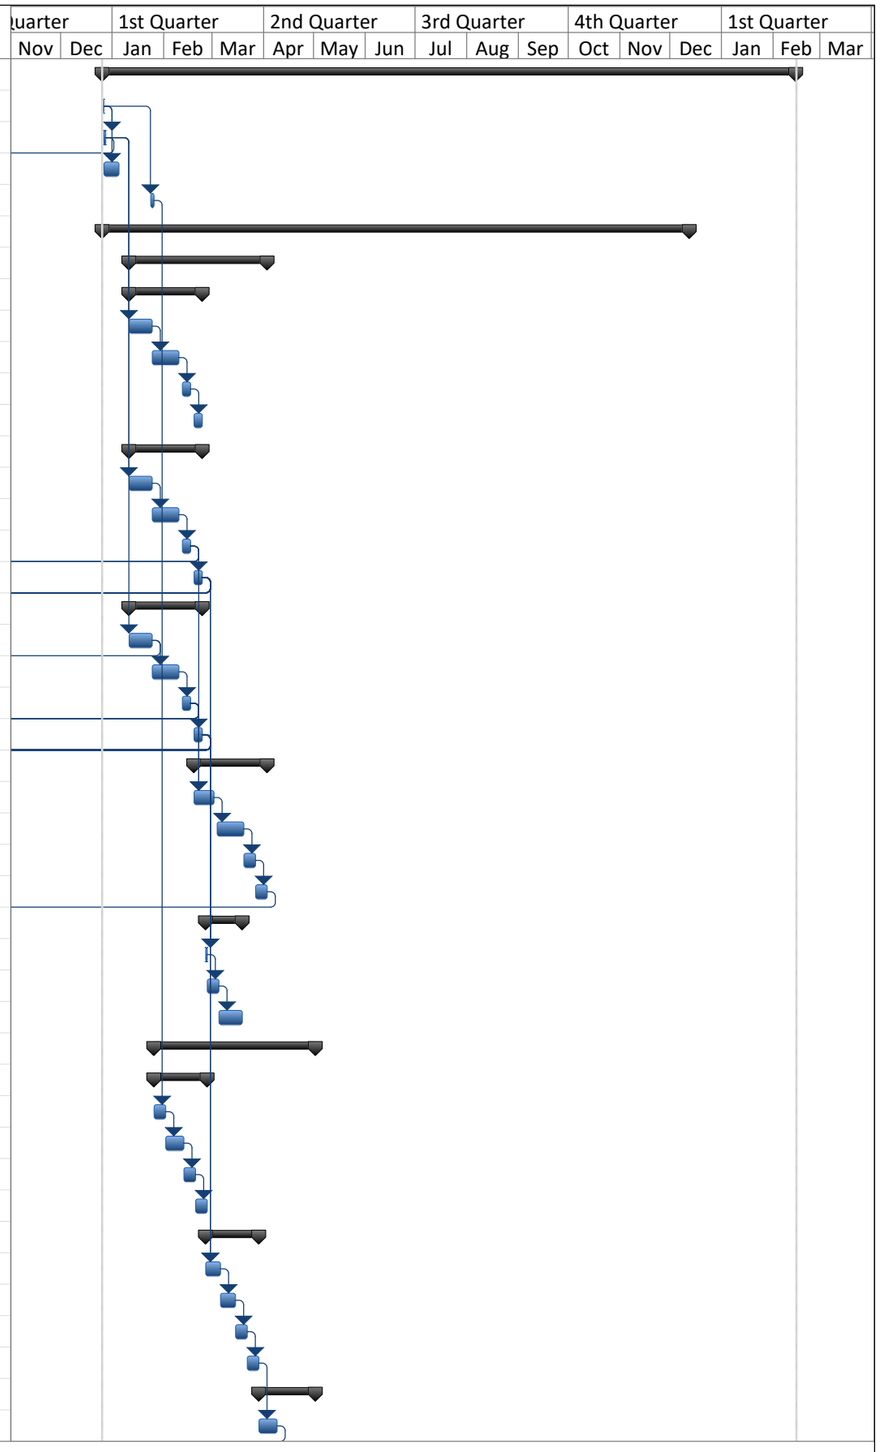

200 m3/hr DM RO Chain at RIL HMD
Start Date: 23.12.26

Task		Project Summary		Inactive Milestone		Manual Summary Rollup		Deadline	
Split		External Tasks		Inactive Summary		Manual Summary		Progress	
Milestone		External Milestone		Manual Task		Start-only			
Summary		Inactive Task		Duration-only		Finish-only			

ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors
45		Receipt of 1st comments	7 days	09 Apr '24	17 Apr '24	44
46		Re-submission	5 days	18 Apr '24	24 Apr '24	45
47		Final Approval	5 days	25 Apr '24	01 May '24	46
48		**Detail Engineering- Mechanical**	**138 days**	**11 Jan '24**	**22 Jul '24**	
49		**Equipment Layout**	**32 days**	**11 Jan '24**	**23 Feb '24**	
50		Submission	10 days	11 Jan '24	24 Jan '24	3FS+10 days
51		Receipt of 1st comments	12 days	25 Jan '24	09 Feb '24	50
52		Re-submission	5 days	12 Feb '24	16 Feb '24	51
53		Final Approval	5 days	19 Feb '24	23 Feb '24	52
54		**UF Permeate (Filterate) Tank Foundations**	**59 days**	**28 Feb '24**	**20 May '24**	
55		Submission of Foundation Details	10 days	28 Feb '24	12 Mar '24	21,52,136
56		Receipt of 1st comments	12 days	13 Mar '24	28 Mar '24	55
57		Re-submission	5 days	29 Mar '24	04 Apr '24	56
58		Final Approval	5 days	05 Apr '24	11 Apr '24	57
59		Submission of RCC Drawing & Design Calculations	10 days	05 Apr '24	18 Apr '24	57
60		Receipt of 1st comments	12 days	19 Apr '24	06 May '24	59
61		Re-submission	5 days	07 May '24	13 May '24	60
62		Final Approval	5 days	14 May '24	20 May '24	61
63		**Degassed Water Storage Tank Foundations**	**59 days**	**28 Feb '24**	**20 May '24**	
64		Submission of Foundation Details	10 days	28 Feb '24	12 Mar '24	21,52,151
65		Receipt of 1st comments	12 days	13 Mar '24	28 Mar '24	64
66		Re-submission	5 days	29 Mar '24	04 Apr '24	65
67		Final Approval	5 days	05 Apr '24	11 Apr '24	66
68		Submission of RCC Drawing & Design Calculations	10 days	05 Apr '24	18 Apr '24	66
69		Receipt of 1st comments	12 days	19 Apr '24	06 May '24	68
70		Re-submission	5 days	07 May '24	13 May '24	69
71		Final Approval	5 days	14 May '24	20 May '24	70
72		**Neutralization Pit**	**59 days**	**15 Mar '24**	**05 Jun '24**	
73		Submission Of Civil Assignment drawings	10 days	15 Mar '24	28 Mar '24	55FS+2 days,64FS+2 days
74		Receipt of 1st comments	12 days	29 Mar '24	15 Apr '24	73
75		Re-submission	5 days	16 Apr '24	22 Apr '24	74
76		Final Approval	5 days	23 Apr '24	29 Apr '24	75
77		Submission of RCC Drawing & Design Calculations	10 days	23 Apr '24	06 May '24	75
78		Receipt of 1st comments	12 days	07 May '24	22 May '24	77
79		Re-submission	5 days	23 May '24	29 May '24	78
80		Final Approval	5 days	30 May '24	05 Jun '24	79
81		**PEB Shed**	**32 days**	**03 Apr '24**	**16 May '24**	
82		Submission of RCC Drawing & Design Calculations	10 days	03 Apr '24	16 Apr '24	119
83		Receipt of 1st comments	12 days	17 Apr '24	02 May '24	82
84		Re-submission	5 days	03 May '24	09 May '24	83
85		Final Approval	5 days	10 May '24	16 May '24	84
86		**Degasser Tower Platform**	**59 days**	**12 Apr '24**	**03 Jul '24**	
87		Submission of Foundation Details	10 days	12 Apr '24	25 Apr '24	73FS+2 days,180,324
88		Receipt of 1st comments	12 days	26 Apr '24	13 May '24	87

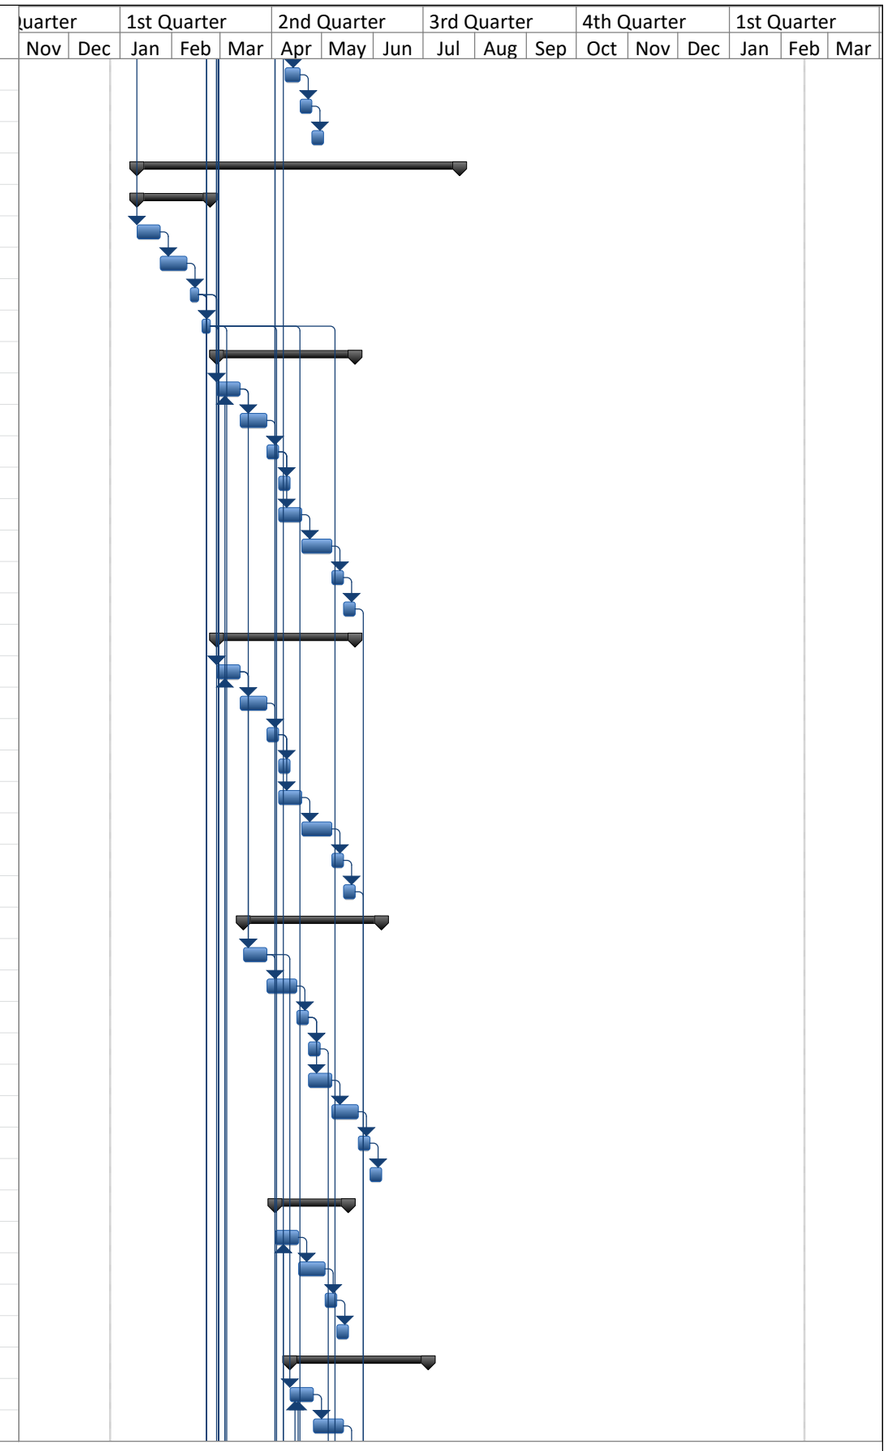

200 m3/hr DM RO Chain at RIL HMD
Start Date: 23.12.26

Task		Project Summary		Inactive Milestone		Manual Summary Rollup		Deadline	
Split		External Tasks		Inactive Summary		Manual Summary		Progress	
Milestone		External Milestone		Manual Task		Start-only			
Summary		Inactive Task		Duration-only		Finish-only			

ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors
89		Re-submission	5 days	14 May '24	20 May '24	88
90		Final Approval	5 days	21 May '24	27 May '24	89
91		Submission of RCC Drawing & Design Calculations	10 days	21 May '24	03 Jun '24	89
92		Receipt of 1st comments	12 days	04 Jun '24	19 Jun '24	91
93		Re-submission	5 days	20 Jun '24	26 Jun '24	92
94		Final Approval	5 days	27 Jun '24	03 Jul '24	93
95		**Static Equipment Foundation Details**	**59 days**	**17 Apr '24**	**08 Jul '24**	
96		Submission of Foundation Details	10 days	17 Apr '24	30 Apr '24	171,189,198,207,226,240,2
97		Receipt of 1st comments	12 days	01 May '24	16 May '24	96
98		Re-submission	5 days	17 May '24	23 May '24	97
99		Final Approval	5 days	24 May '24	30 May '24	98
100		Submission of RCC Drawing & Design Calculations	10 days	24 May '24	06 Jun '24	98
101		Receipt of 1st comments	12 days	07 Jun '24	24 Jun '24	100
102		Re-submission	5 days	25 Jun '24	01 Jul '24	101
103		Final Approval	5 days	02 Jul '24	08 Jul '24	102
104		**Rotary Equipment Foundation Details**	**59 days**	**01 May '24**	**22 Jul '24**	
105		Submission of Foundation Details	10 days	01 May '24	14 May '24	282,296,310,338,352,96
106		Receipt of 1st comments	12 days	15 May '24	30 May '24	105
107		Re-submission	5 days	31 May '24	06 Jun '24	106
108		Final Approval	5 days	07 Jun '24	13 Jun '24	107
109		Submission of RCC Drawing & Design Calculations	10 days	07 Jun '24	20 Jun '24	107
110		Receipt of 1st comments	12 days	21 Jun '24	08 Jul '24	109
111		Re-submission	5 days	09 Jul '24	15 Jul '24	110
112		Final Approval	5 days	16 Jul '24	22 Jul '24	111
113		**Mechanical Engineering & Procurement**	**198.75 days**	**19 Feb '24**	**21 Nov '24**	
114		**Pre-Engineered Building**	**140.75 days**	**19 Feb '24**	**02 Sep '24**	
115		Release of Enquiry	2 days	19 Feb '24	20 Feb '24	52
116		Receipt of Offers	10 days	21 Feb '24	05 Mar '24	115
117		Technical Clearance for Ordering	3 days	06 Mar '24	08 Mar '24	116
118		Ordering	7 days	11 Mar '24	19 Mar '24	117
119		Receipt of Post Order Documents from Vendor	10 days	20 Mar '24	02 Apr '24	118
120		**GA Drawing**	**22 days**	**03 Apr '24**	**02 May '24**	
121		Submission	2 days	03 Apr '24	04 Apr '24	119
122		Receipt of 1st comments	10 days	05 Apr '24	18 Apr '24	121
123		Re-submission	5 days	19 Apr '24	25 Apr '24	122
124		Final Approval	5 days	26 Apr '24	02 May '24	123
125		**Fabrication Drawing**	**22 days**	**03 Apr '24**	**02 May '24**	
126		Submission	2 days	03 Apr '24	04 Apr '24	119
127		Receipt of 1st comments	10 days	05 Apr '24	18 Apr '24	126
128		Re-submission	5 days	19 Apr '24	25 Apr '24	127
129		Final Approval	5 days	26 Apr '24	02 May '24	128
130		Manufacturing Clearance	1 day	26 Apr '24	26 Apr '24	123,128
131		Manufacturing	110 days	26 Apr '24	19 Aug '24	130
132		Inspection & Dispatch Clearance	7 days	19 Aug '24	28 Aug '24	131

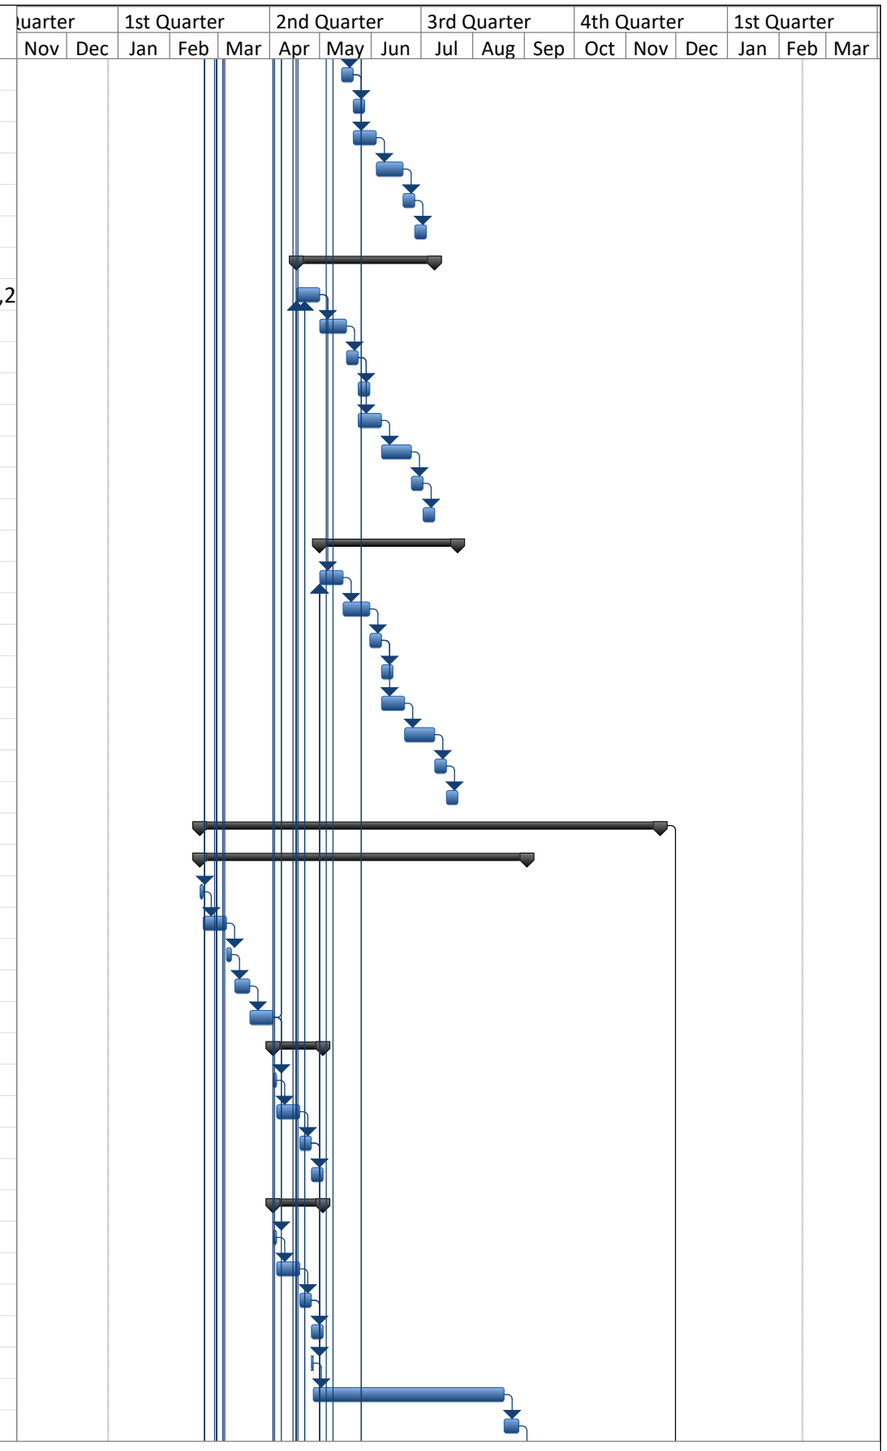

200 m3/hr DM RO Chain at RIL HMD
Start Date: 23.12.26

Task		Project Summary		Inactive Milestone		Manual Summary Rollup		Deadline	
Split		External Tasks		Inactive Summary		Manual Summary		Progress	
Milestone		External Milestone		Manual Task		Start-only			
Summary		Inactive Task		Duration-only		Finish-only			

ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors
133		Receipt At Site	3 days	28 Aug '24	02 Sep '24	132
134		**UF Permeate (Filterate) Storage Tank**	**124 days**	**19 Feb '24**	**08 Aug '24**	
135		**Thickness Calculations**	**27 days**	**19 Feb '24**	**26 Mar '24**	
136		Submission	7 days	19 Feb '24	27 Feb '24	52,21
137		Receipt of 1st comments	10 days	28 Feb '24	12 Mar '24	136
138		Re-submission	5 days	13 Mar '24	19 Mar '24	137
139		Final Approval	5 days	20 Mar '24	26 Mar '24	138
140		**GA Drawing**	**25 days**	**27 Mar '24**	**30 Apr '24**	
141		Submission	5 days	27 Mar '24	02 Apr '24	139
142		Receipt of 1st comments	10 days	03 Apr '24	16 Apr '24	141
143		Re-submission	5 days	17 Apr '24	23 Apr '24	142
144		Final Approval	5 days	24 Apr '24	30 Apr '24	143
145		Release of BOQ for Tank	5 days	01 May '24	07 May '24	144
146		Ordering of Raw Material for Tank	7 days	08 May '24	16 May '24	145
147		Inspection & Dispatch Clearance of Raw Material for Tanl	30 days	17 May '24	27 Jun '24	146
148		Receipt At Site	30 days	28 Jun '24	08 Aug '24	147
149		**Degassed Water Storage Tank**	**124 days**	**19 Feb '24**	**08 Aug '24**	
150		**Thickness Calculations**	**27 days**	**19 Feb '24**	**26 Mar '24**	
151		Submission	7 days	19 Feb '24	27 Feb '24	52,21
152		Receipt of 1st comments	10 days	28 Feb '24	12 Mar '24	151
153		Re-submission	5 days	13 Mar '24	19 Mar '24	152
154		Final Approval	5 days	20 Mar '24	26 Mar '24	153
155		**GA Drawing**	**25 days**	**27 Mar '24**	**30 Apr '24**	
156		Submission	5 days	27 Mar '24	02 Apr '24	154
157		Receipt of 1st comments	10 days	03 Apr '24	16 Apr '24	156
158		Re-submission	5 days	17 Apr '24	23 Apr '24	157
159		Final Approval	5 days	24 Apr '24	30 Apr '24	158
160		Release of BOQ for Tank	5 days	01 May '24	07 May '24	159
161		Ordering of Raw Material for Tank	7 days	08 May '24	16 May '24	160
162		Inspection & Dispatch Clearance of Raw Material for Tanl	30 days	17 May '24	27 Jun '24	161
163		Receipt At Site	30 days	28 Jun '24	08 Aug '24	162
164		**MB Vessels**	**91.25 days**	**28 Feb '24**	**04 Jul '24**	
165		**Thickness Calculations**	**25 days**	**28 Feb '24**	**02 Apr '24**	
166		Submission	5 days	28 Feb '24	05 Mar '24	136,19
167		Receipt of 1st comments	10 days	06 Mar '24	19 Mar '24	166
168		Re-submission	5 days	20 Mar '24	26 Mar '24	167
169		Final Approval	5 days	27 Mar '24	02 Apr '24	168
170		**GA Drawing**	**25 days**	**06 Mar '24**	**09 Apr '24**	
171		Submission	5 days	06 Mar '24	12 Mar '24	166
172		Receipt of 1st comments	10 days	13 Mar '24	26 Mar '24	171
173		Re-submission	5 days	27 Mar '24	02 Apr '24	172
174		Final Approval	5 days	03 Apr '24	09 Apr '24	173
175		Ordering & clearance for Fabrication of MB Vessels	5 days	03 Apr '24	09 Apr '24	173
176		Fabrication	60 days	09 Apr '24	11 Jun '24	175

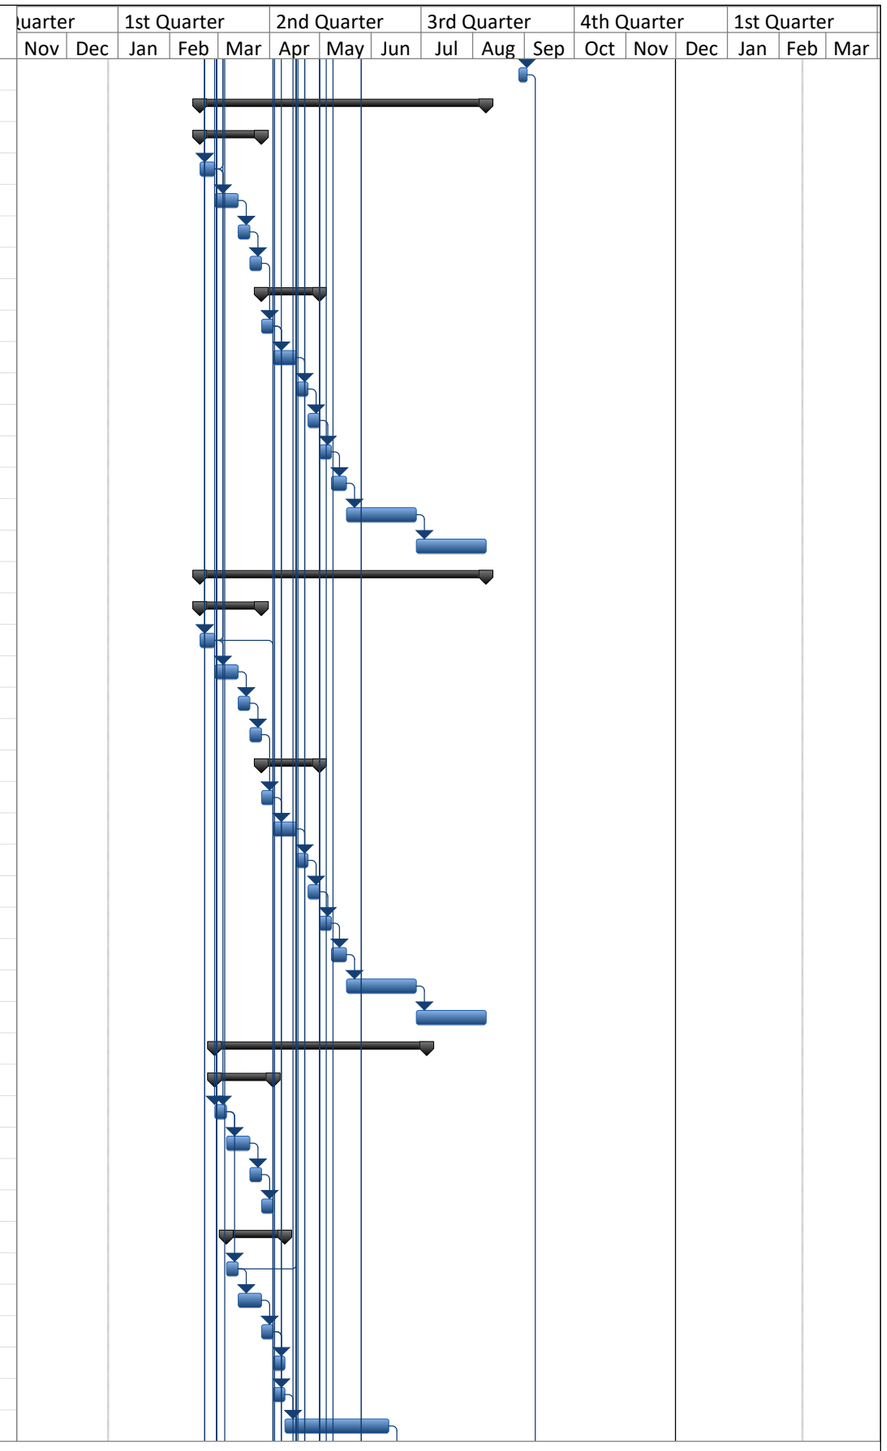

200 m3/hr DM RO Chain at RIL HMD
Start Date: 23.12.26

Task		Project Summary		Inactive Milestone		Manual Summary Rollup		Deadline	
Split		External Tasks		Inactive Summary		Manual Summary		Progress	
Milestone		External Milestone		Manual Task		Start-only			
Summary		Inactive Task		Duration-only		Finish-only			

ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors
177		Inspection & Dispatch Clearance	10 days	11 Jun '24	25 Jun '24	176
178		Receipt At site	7 days	25 Jun '24	04 Jul '24	177
179		**Degasser Tower**	**75 days**	**03 Apr '24**	**16 Jul '24**	
180		Submission of GA Drawing	5 days	03 Apr '24	09 Apr '24	141,151
181		Receipt of 1st comments	10 days	10 Apr '24	23 Apr '24	180
182		Re-submission	5 days	24 Apr '24	30 Apr '24	181
183		Final Approval	5 days	01 May '24	07 May '24	182
184		Ordering & clearance for Fabrication	5 days	01 May '24	07 May '24	182
185		Fabrication	45 days	07 May '24	22 Jun '24	184
186		Inspection & Dispatch Clearance	10 days	24 Jun '24	05 Jul '24	185
187		Receipt At site	7 days	08 Jul '24	16 Jul '24	186
188		**RO Skid**	**71.5 days**	**10 Apr '24**	**18 Jul '24**	
189		Submission of GA Drawing	5 days	10 Apr '24	16 Apr '24	180
190		Receipt of 1st comments	10 days	17 Apr '24	30 Apr '24	189
191		Re-submission	5 days	01 May '24	07 May '24	190
192		Final Approval	5 days	08 May '24	14 May '24	191
193		Ordering & clearance for Fabrication	5 days	08 May '24	14 May '24	191
194		Fabrication	40 days	14 May '24	25 Jun '24	193
195		Inspection & Dispatch Clearance	10 days	25 Jun '24	09 Jul '24	194
196		Receipt At site	7 days	09 Jul '24	18 Jul '24	195
197		**Priming Vessel for Neutralised Effluent Transfer Pumps**	**71.5 days**	**10 Apr '24**	**18 Jul '24**	
198		Submission of GA Drawing	5 days	10 Apr '24	16 Apr '24	189SS
199		Receipt of 1st comments	10 days	17 Apr '24	30 Apr '24	198
200		Re-submission	5 days	01 May '24	07 May '24	199
201		Final Approval	5 days	08 May '24	14 May '24	200
202		Ordering & clearance for Fabrication	5 days	08 May '24	14 May '24	200
203		Fabrication	40 days	14 May '24	25 Jun '24	202
204		Inspection & Dispatch Clearance	10 days	25 Jun '24	09 Jul '24	203
205		Receipt At site	7 days	09 Jul '24	18 Jul '24	204
206		**Auto Backwash Filters**	**133 days**	**26 Feb '24**	**28 Aug '24**	
207		Release of Enquiry	5 days	26 Feb '24	01 Mar '24	17,22
208		Receipt of Offers	7 days	04 Mar '24	12 Mar '24	207
209		Technical Clearance for Ordering	5 days	13 Mar '24	19 Mar '24	208
210		Ordering	5 days	20 Mar '24	26 Mar '24	209
211		Receipt of Post Order Documents from Vendor	7 days	27 Mar '24	04 Apr '24	210
212		Submission of Documents	5 days	05 Apr '24	11 Apr '24	211
213		Receipt of 1st comments	10 days	12 Apr '24	25 Apr '24	212
214		Re-submission	5 days	26 Apr '24	02 May '24	213
215		Final Approval	5 days	03 May '24	09 May '24	214
216		Manufacturing Clearance	1 day	03 May '24	03 May '24	214
217		Manufacturing	90 days	03 May '24	05 Aug '24	216
218		Inspection & Dispatch Clearance	10 days	06 Aug '24	19 Aug '24	217
219		Receipt At site	7 days	20 Aug '24	28 Aug '24	218
220		**Basket Filters-UF & UF CIP**	**111.25 days**	**26 Feb '24**	**30 Jul '24**	

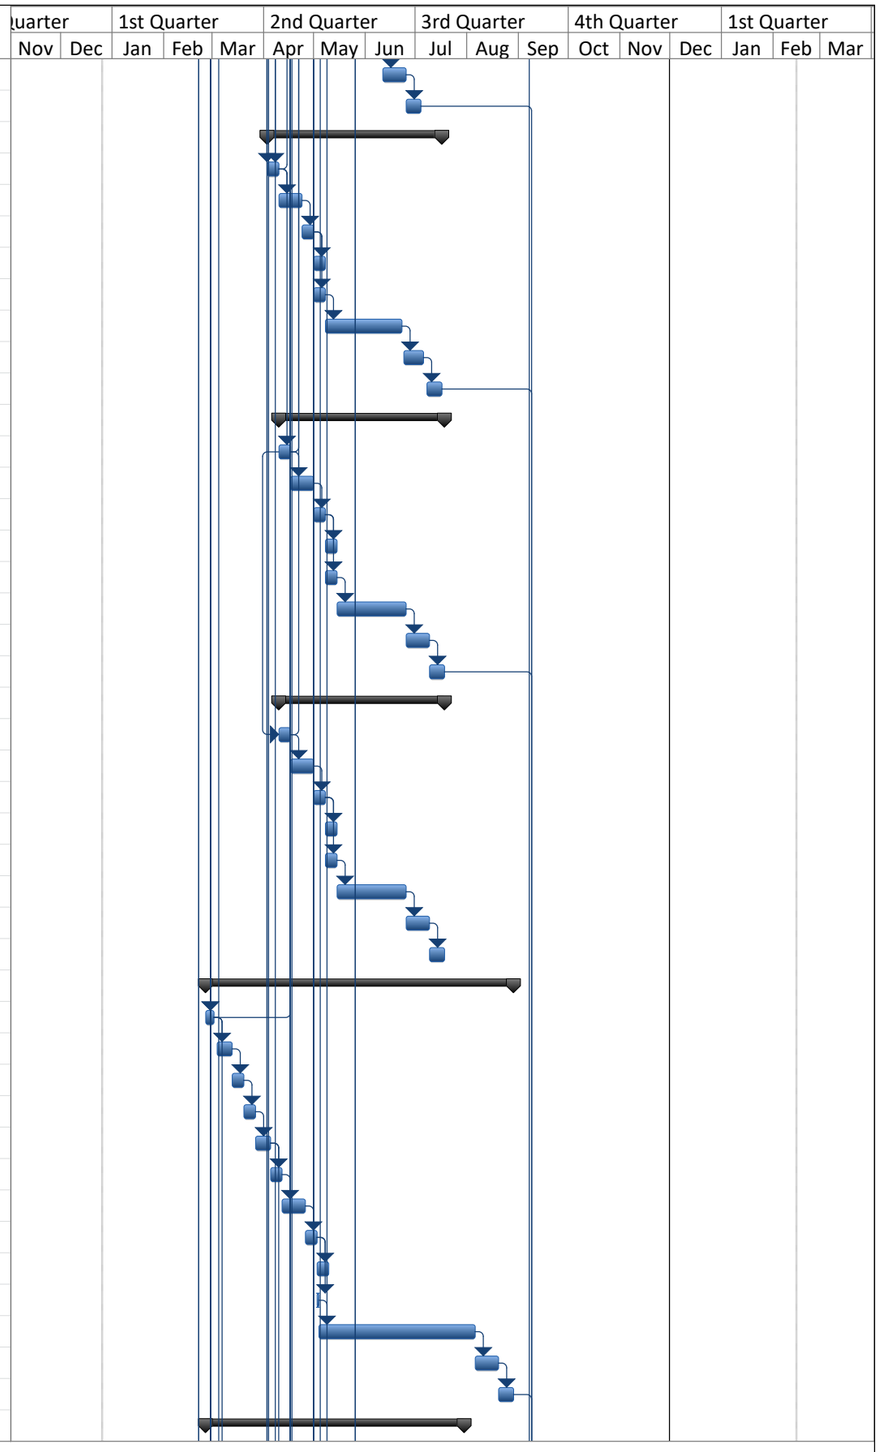

200 m3/hr DM RO Chain at RIL HMD
Start Date: 23.12.26

Task	Project Summary	Inactive Milestone	Manual Summary Rollup	Deadline
Split	External Tasks	Inactive Summary	Manual Summary	Progress
Milestone	External Milestone	Manual Task	Start-only	
Summary	Inactive Task	Duration-only	Finish-only	

ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors
221		Release of Enquiry	5 days	26 Feb '24	01 Mar '24	17,22
222		Receipt of Offers	7 days	04 Mar '24	12 Mar '24	221
223		Technical Clearance for Ordering	5 days	13 Mar '24	19 Mar '24	222
224		Ordering	5 days	20 Mar '24	26 Mar '24	223
225		Receipt of Post Order Documents from Vendor	7 days	27 Mar '24	04 Apr '24	224
226		Submission of Documents	5 days	05 Apr '24	11 Apr '24	225
227		Receipt of 1st comments	10 days	12 Apr '24	25 Apr '24	226
228		Re-submission	5 days	26 Apr '24	02 May '24	227
229		Final Approval	5 days	03 May '24	09 May '24	228
230		Manufacturing Clearance	1 day	03 May '24	03 May '24	228
231		Manufacturing	60 days	03 May '24	05 Jul '24	230
232		Inspection & Dispatch Clearance	10 days	05 Jul '24	19 Jul '24	231
233		Receipt At site	7 days	19 Jul '24	30 Jul '24	232
234		**UF Modules**	**81.5 days**	**26 Feb '24**	**18 Jun '24**	
235		Release of Enquiry	5 days	26 Feb '24	01 Mar '24	17,22
236		Receipt of Offers	7 days	04 Mar '24	12 Mar '24	235
237		Technical Clearance for Ordering	5 days	13 Mar '24	19 Mar '24	236
238		Ordering	5 days	20 Mar '24	26 Mar '24	237
239		Receipt of Post Order Documents from Vendor	7 days	27 Mar '24	04 Apr '24	238
240		Submission of Documents	5 days	05 Apr '24	11 Apr '24	239
241		Receipt of 1st comments	10 days	12 Apr '24	25 Apr '24	240
242		Re-submission	5 days	26 Apr '24	02 May '24	241
243		Final Approval	5 days	03 May '24	09 May '24	242
244		Manufacturing Clearance	1 day	12 Apr '24	12 Apr '24	240
245		Manufacturing	40 days	12 Apr '24	24 May '24	244
246		Inspection & Dispatch Clearance	10 days	24 May '24	07 Jun '24	245
247		Receipt At site	7 days	07 Jun '24	18 Jun '24	246
248		**Micron Cartridge Filters-RO & RO CIP**	**100 days**	**26 Feb '24**	**12 Jul '24**	
249		Release of Enquiry	5 days	26 Feb '24	01 Mar '24	17,22
250		Receipt of Offers	7 days	04 Mar '24	12 Mar '24	249
251		Technical Clearance for Ordering	5 days	13 Mar '24	19 Mar '24	250
252		Ordering	5 days	20 Mar '24	26 Mar '24	251
253		Receipt of Post Order Documents from Vendor	7 days	27 Mar '24	04 Apr '24	252
254		Submission of Documents	5 days	05 Apr '24	11 Apr '24	253
255		Receipt of 1st comments	10 days	12 Apr '24	25 Apr '24	254
256		Re-submission	5 days	26 Apr '24	02 May '24	255
257		Final Approval	5 days	03 May '24	09 May '24	256
258		Manufacturing Clearance	1 day	03 May '24	03 May '24	256
259		Manufacturing	45 days	03 May '24	19 Jun '24	258
260		Inspection & Dispatch Clearance	10 days	20 Jun '24	03 Jul '24	259
261		Receipt At site	7 days	04 Jul '24	12 Jul '24	260
262		**RO Membranes**	**103.38 days**	**26 Feb '24**	**18 Jul '24**	
263		Release of Enquiry	5 days	26 Feb '24	01 Mar '24	17,22
264		Receipt of Offers	7 days	04 Mar '24	12 Mar '24	263

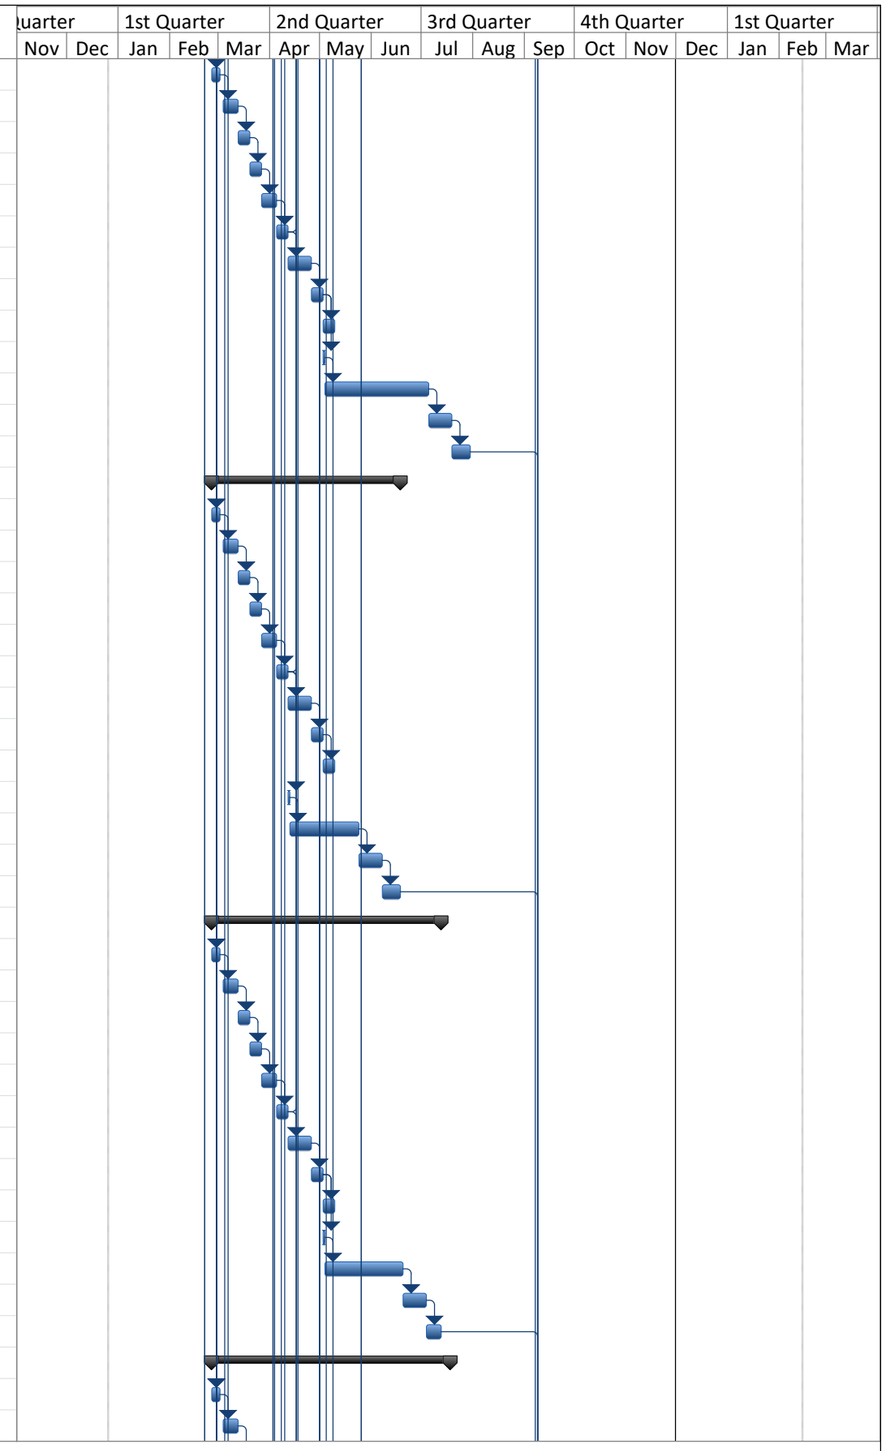

200 m3/hr DM RO Chain at RIL HMD
Start Date: 23.12.26

Task		Project Summary		Inactive Milestone		Manual Summary Rollup		Deadline	
Split		External Tasks		Inactive Summary		Manual Summary		Progress	
Milestone		External Milestone		Manual Task		Start-only			
Summary		Inactive Task		Duration-only		Finish-only			

ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors
265		Technical Clearance for Ordering	5 days	13 Mar '24	19 Mar '24	264
266		Ordering	5 days	20 Mar '24	26 Mar '24	265
267		Receipt of Post Order Documents from Vendor	7 days	27 Mar '24	04 Apr '24	266
268		Submission of Documents	5 days	05 Apr '24	11 Apr '24	267
269		Receipt of 1st comments	10 days	12 Apr '24	25 Apr '24	268
270		Re-submission	5 days	26 Apr '24	02 May '24	269
271		Final Approval	5 days	03 May '24	09 May '24	270
272		Manufacturing Clearance	1 day	03 May '24	03 May '24	270
273		Manufacturing	50 days	03 May '24	25 Jun '24	272
274		Inspection & Dispatch Clearance	10 days	25 Jun '24	09 Jul '24	273
275		Receipt At site	7 days	09 Jul '24	18 Jul '24	274
276		**RO HPP**	**170.38 days**	**26 Feb '24**	**21 Oct '24**	
277		Release of Enquiry	5 days	26 Feb '24	01 Mar '24	17,22
278		Receipt of Offers	7 days	04 Mar '24	12 Mar '24	277
279		Technical Clearance for Ordering	5 days	13 Mar '24	19 Mar '24	278
280		Ordering	5 days	20 Mar '24	26 Mar '24	279
281		Receipt of Post Order Documents from Vendor	7 days	27 Mar '24	04 Apr '24	280
282		Submission of Documents	5 days	05 Apr '24	11 Apr '24	281
283		Receipt of 1st comments	10 days	12 Apr '24	25 Apr '24	282
284		Re-submission	5 days	26 Apr '24	02 May '24	283
285		Final Approval	5 days	03 May '24	09 May '24	284
286		Manufacturing Clearance	1 day	03 May '24	03 May '24	284
287		Manufacturing	140 days	03 May '24	26 Sep '24	286
288		Inspection & Dispatch Clearance	10 days	26 Sep '24	10 Oct '24	287
289		Receipt At site	7 days	10 Oct '24	21 Oct '24	288
290		**Centrifugal Pumps-Metallic**	**147.75 days**	**26 Feb '24**	**18 Sep '24**	
291		Release of Enquiry	5 days	26 Feb '24	01 Mar '24	17,22
292		Receipt of Offers	7 days	04 Mar '24	12 Mar '24	291
293		Technical Clearance for Ordering	5 days	13 Mar '24	19 Mar '24	292
294		Ordering	5 days	20 Mar '24	26 Mar '24	293
295		Receipt of Post Order Documents from Vendor	7 days	27 Mar '24	04 Apr '24	294
296		Submission of Documents	5 days	05 Apr '24	11 Apr '24	295
297		Receipt of 1st comments	10 days	12 Apr '24	25 Apr '24	296
298		Re-submission	5 days	26 Apr '24	02 May '24	297
299		Final Approval	5 days	03 May '24	09 May '24	298
300		Manufacturing Clearance	1 day	03 May '24	03 May '24	298
301		Manufacturing	110 days	03 May '24	26 Aug '24	300
302		Inspection & Dispatch Clearance	10 days	26 Aug '24	09 Sep '24	301
303		Receipt At site	7 days	09 Sep '24	18 Sep '24	302
304		**Centrifugal Pumps-Non Metallic**	**106.25 days**	**26 Feb '24**	**23 Jul '24**	
305		Release of Enquiry	5 days	26 Feb '24	01 Mar '24	17,22
306		Receipt of Offers	7 days	04 Mar '24	12 Mar '24	305
307		Technical Clearance for Ordering	5 days	13 Mar '24	19 Mar '24	306
308		Ordering	5 days	20 Mar '24	26 Mar '24	307

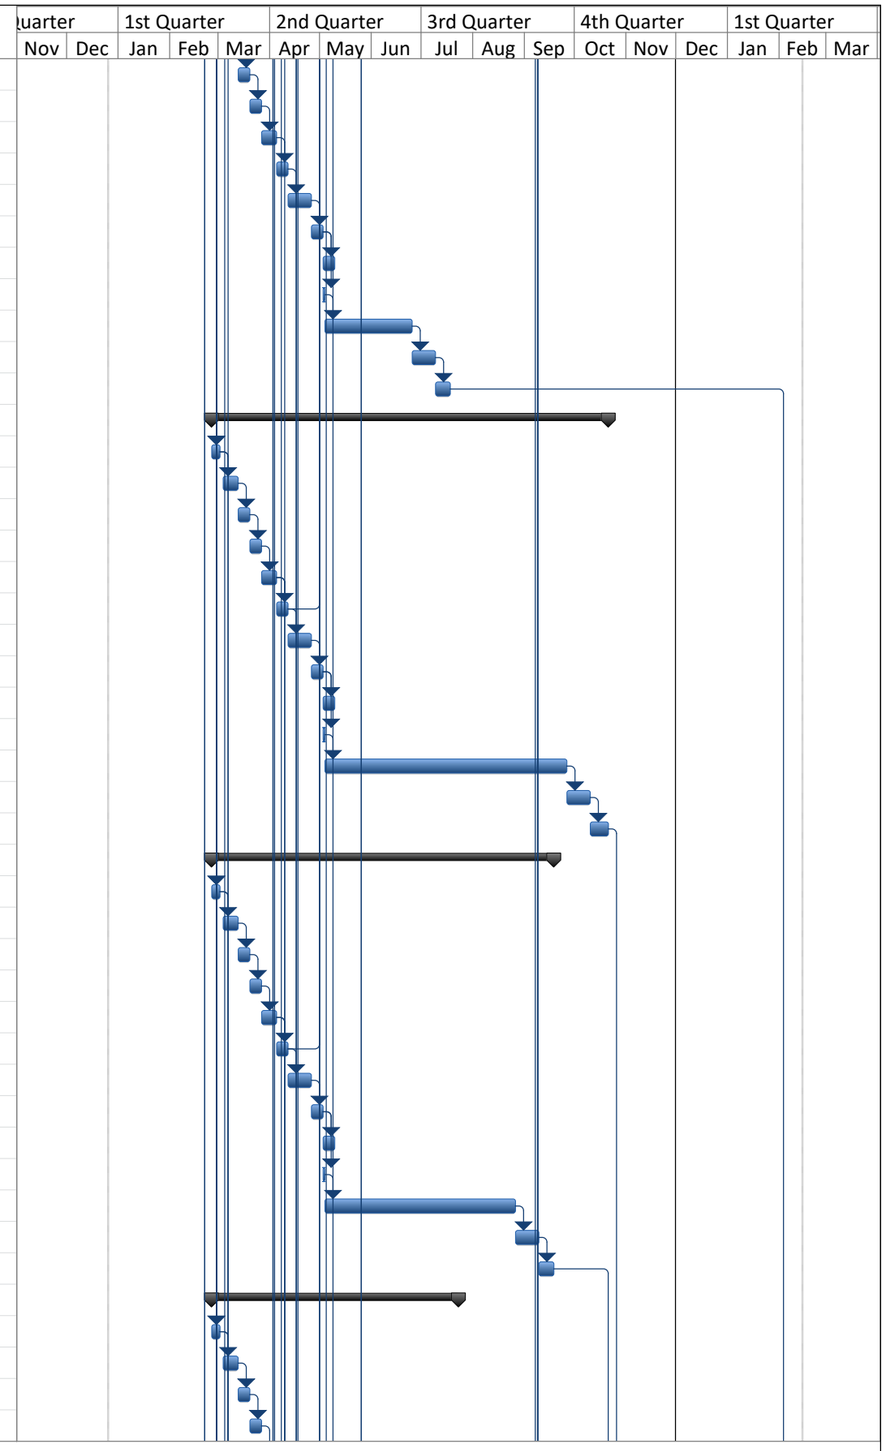

200 m3/hr DM RO Chain at RIL HMD
Start Date: 23.12.26

Task		Project Summary		Inactive Milestone		Manual Summary Rollup		Deadline	
Split		External Tasks		Inactive Summary		Manual Summary		Progress	
Milestone		External Milestone		Manual Task		Start-only			
Summary		Inactive Task		Duration-only		Finish-only			

ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors
309		Receipt of Post Order Documents from Vendor	7 days	27 Mar '24	04 Apr '24	308
310		Submission of Documents	5 days	05 Apr '24	11 Apr '24	309
311		Receipt of 1st comments	10 days	12 Apr '24	25 Apr '24	310
312		Re-submission	5 days	26 Apr '24	02 May '24	311
313		Final Approval	5 days	03 May '24	09 May '24	312
314		Manufacturing Clearance	1 day	26 Apr '24	26 Apr '24	311
315		Manufacturing	60 days	26 Apr '24	28 Jun '24	314
316		Inspection & Dispatch Clearance	10 days	28 Jun '24	12 Jul '24	315
317		Receipt At site	7 days	12 Jul '24	23 Jul '24	316
318		**Centrifugal Blowers**	**140.88 days**	**26 Feb '24**	**09 Sep '24**	
319		Release of Enquiry	5 days	26 Feb '24	01 Mar '24	17,22
320		Receipt of Offers	7 days	04 Mar '24	12 Mar '24	319
321		Technical Clearance for Ordering	5 days	13 Mar '24	19 Mar '24	320
322		Ordering	5 days	20 Mar '24	26 Mar '24	321
323		Receipt of Post Order Documents from Vendor	7 days	27 Mar '24	04 Apr '24	322
324		Submission of Documents	5 days	05 Apr '24	11 Apr '24	323
325		Receipt of 1st comments	10 days	12 Apr '24	25 Apr '24	324
326		Re-submission	5 days	26 Apr '24	02 May '24	325
327		Final Approval	5 days	03 May '24	09 May '24	326
328		Manufacturing Clearance	1 day	03 May '24	03 May '24	326
329		Manufacturing	100 days	03 May '24	15 Aug '24	328
330		Inspection & Dispatch Clearance	10 days	15 Aug '24	29 Aug '24	329
331		Receipt At site	7 days	29 Aug '24	09 Sep '24	330
332		**Twin-Lobe Blowers**	**140.88 days**	**26 Feb '24**	**09 Sep '24**	
333		Release of Enquiry	5 days	26 Feb '24	01 Mar '24	17,22
334		Receipt of Offers	7 days	04 Mar '24	12 Mar '24	333
335		Technical Clearance for Ordering	5 days	13 Mar '24	19 Mar '24	334
336		Ordering	5 days	20 Mar '24	26 Mar '24	335
337		Receipt of Post Order Documents from Vendor	7 days	27 Mar '24	04 Apr '24	336
338		Submission of Documents	5 days	05 Apr '24	11 Apr '24	337
339		Receipt of 1st comments	10 days	12 Apr '24	25 Apr '24	338
340		Re-submission	5 days	26 Apr '24	02 May '24	339
341		Final Approval	5 days	03 May '24	09 May '24	340
342		Manufacturing Clearance	1 day	03 May '24	03 May '24	340
343		Manufacturing	100 days	03 May '24	15 Aug '24	342
344		Inspection & Dispatch Clearance	10 days	15 Aug '24	29 Aug '24	343
345		Receipt At site	7 days	29 Aug '24	09 Sep '24	344
346		**Dosing Pumps**	**140.88 days**	**26 Feb '24**	**09 Sep '24**	
347		Release of Enquiry	5 days	26 Feb '24	01 Mar '24	17,22
348		Receipt of Offers	7 days	04 Mar '24	12 Mar '24	347
349		Technical Clearance for Ordering	5 days	13 Mar '24	19 Mar '24	348
350		Ordering	5 days	20 Mar '24	26 Mar '24	349
351		Receipt of Post Order Documents from Vendor	7 days	27 Mar '24	04 Apr '24	350
352		Submission of Documents	5 days	05 Apr '24	11 Apr '24	351

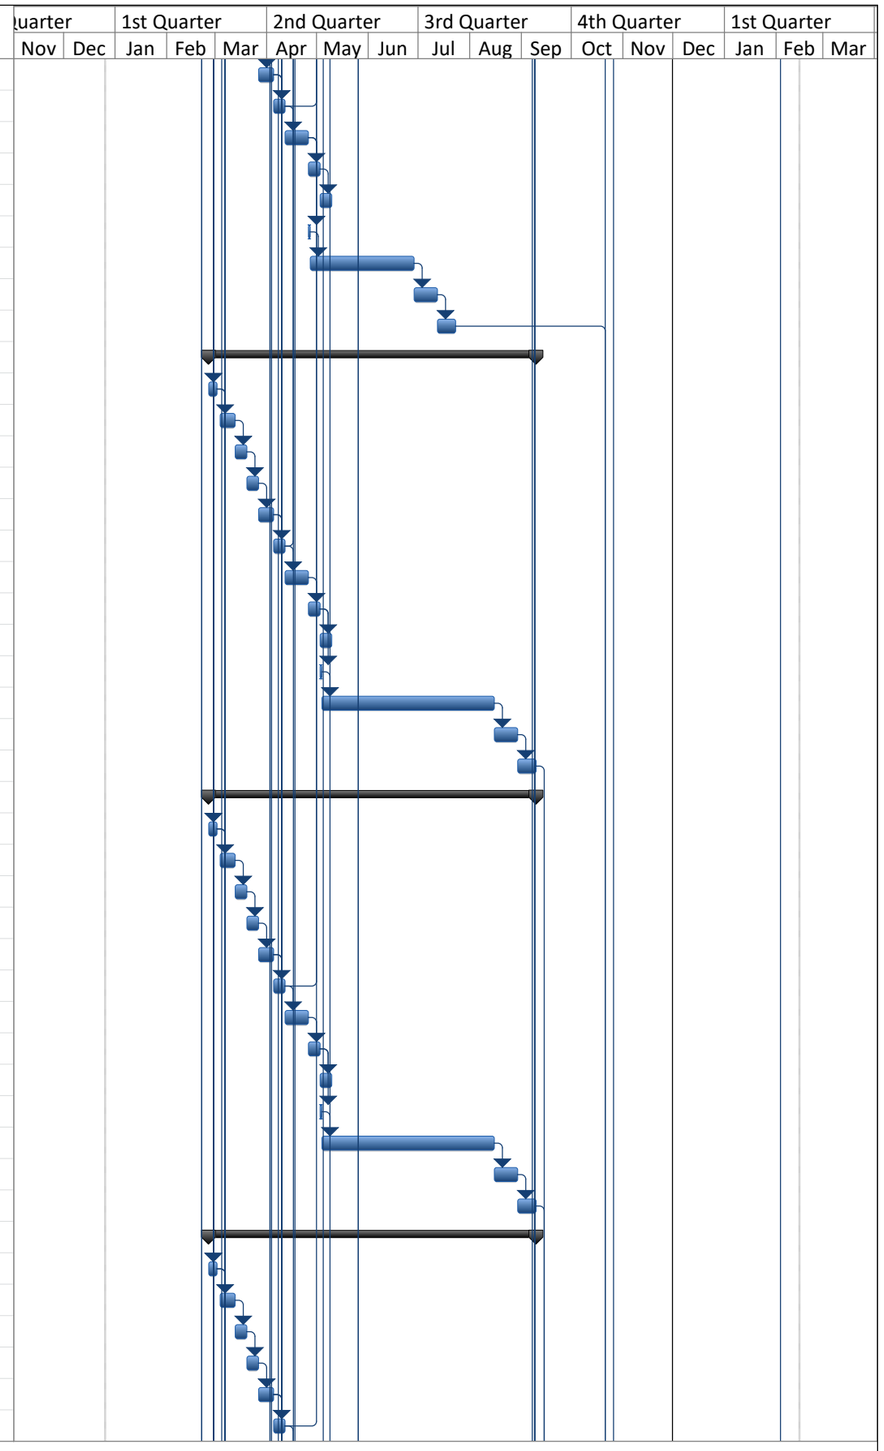

200 m3/hr DM RO Chain at RIL HMD
Start Date: 23.12.26

Task		Project Summary		Inactive Milestone		Manual Summary Rollup		Deadline	
Split		External Tasks		Inactive Summary		Manual Summary		Progress	
Milestone		External Milestone		Manual Task		Start-only			
Summary		Inactive Task		Duration-only		Finish-only			

ID	Task Name	Duration	Start	Finish	Predecessors
353	Receipt of 1st comments	10 days	12 Apr '24	25 Apr '24	352
354	Re-submission	5 days	26 Apr '24	02 May '24	353
355	Final Approval	5 days	03 May '24	09 May '24	354
356	Manufacturing Clearance	1 day	03 May '24	03 May '24	354
357	Manufacturing	100 days	03 May '24	15 Aug '24	356
358	Inspection & Dispatch Clearance	10 days	15 Aug '24	29 Aug '24	357
359	Receipt At site	7 days	29 Aug '24	09 Sep '24	358
360	**Agitators**	**140.88 days**	**26 Feb '24**	**09 Sep '24**	
361	Release of Enquiry	5 days	26 Feb '24	01 Mar '24	17,22
362	Receipt of Offers	7 days	04 Mar '24	12 Mar '24	361
363	Technical Clearance for Ordering	5 days	13 Mar '24	19 Mar '24	362
364	Ordering	5 days	20 Mar '24	26 Mar '24	363
365	Receipt of Post Order Documents from Vendor	7 days	27 Mar '24	04 Apr '24	364
366	Submission of Documents	5 days	05 Apr '24	11 Apr '24	365
367	Receipt of 1st comments	10 days	12 Apr '24	25 Apr '24	366
368	Re-submission	5 days	26 Apr '24	02 May '24	367
369	Final Approval	5 days	03 May '24	09 May '24	368
370	Manufacturing Clearance	1 day	03 May '24	03 May '24	368
371	Manufacturing	100 days	03 May '24	15 Aug '24	370
372	Inspection & Dispatch Clearance	10 days	15 Aug '24	29 Aug '24	371
373	Receipt At site	7 days	29 Aug '24	09 Sep '24	372
374	**Non-Metallic Tanks**	**133 days**	**26 Feb '24**	**28 Aug '24**	
375	Release of Enquiry	5 days	26 Feb '24	01 Mar '24	17,22
376	Receipt of Offers	7 days	04 Mar '24	12 Mar '24	375
377	Technical Clearance for Ordering	5 days	13 Mar '24	19 Mar '24	376
378	Ordering	5 days	20 Mar '24	26 Mar '24	377
379	Receipt of Post Order Documents from Vendor	7 days	27 Mar '24	04 Apr '24	378
380	Submission of Documents	5 days	05 Apr '24	11 Apr '24	379
381	Receipt of 1st comments	10 days	12 Apr '24	25 Apr '24	380
382	Re-submission	5 days	26 Apr '24	02 May '24	381
383	Final Approval	5 days	03 May '24	09 May '24	382
384	Manufacturing Clearance	1 day	03 May '24	03 May '24	382
385	Manufacturing	90 days	03 May '24	05 Aug '24	384
386	Inspection & Dispatch Clearance	10 days	06 Aug '24	19 Aug '24	385
387	Receipt At site	7 days	20 Aug '24	28 Aug '24	386
388	**Valves**	**177.63 days**	**19 Feb '24**	**23 Oct '24**	
389	Submission of Valve Schedule	7 days	19 Feb '24	27 Feb '24	16
390	Receipt of 1st comments	10 days	28 Feb '24	12 Mar '24	389
391	Re-submission	5 days	13 Mar '24	19 Mar '24	390
392	Final Approval	5 days	20 Mar '24	26 Mar '24	391
393	**BF Valves**	**155.63 days**	**20 Mar '24**	**23 Oct '24**	
394	Release of Enquiry	5 days	20 Mar '24	26 Mar '24	391
395	Receipt of Offers	7 days	27 Mar '24	04 Apr '24	394
396	Technical Clearance for Ordering	5 days	05 Apr '24	11 Apr '24	395

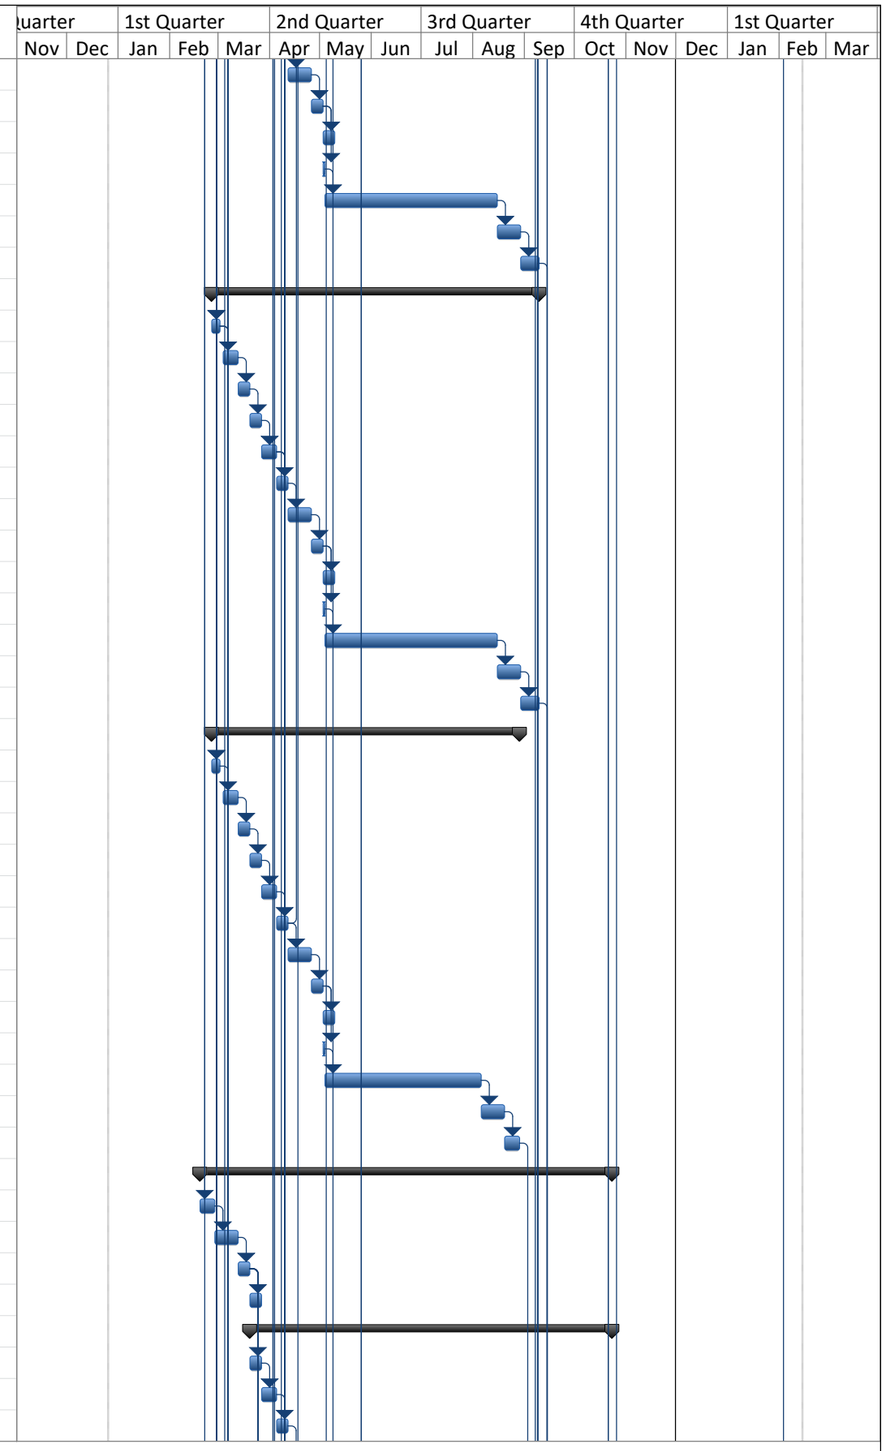

200 m3/hr DM RO Chain at RIL HMD
Start Date: 23.12.26

Task		Project Summary		Inactive Milestone		Manual Summary Rollup		Deadline	
Split		External Tasks		Inactive Summary		Manual Summary		Progress	
Milestone		External Milestone		Manual Task		Start-only			
Summary		Inactive Task		Duration-only		Finish-only			

ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors
397		Ordering	5 days	12 Apr '24	18 Apr '24	396
398		Receipt of Post Order Documents from Vendor	7 days	19 Apr '24	29 Apr '24	397
399		Submission of Documents	5 days	30 Apr '24	06 May '24	398
400		Receipt of 1st comments	10 days	07 May '24	20 May '24	399
401		Re-submission	5 days	21 May '24	27 May '24	400
402		Final Approval	5 days	28 May '24	03 Jun '24	401
403		Manufacturing Clearance	1 day	28 May '24	28 May '24	401
404		Manufacturing	120 days	28 May '24	30 Sep '24	403
405		Inspection & Dispatch Clearance	10 days	30 Sep '24	14 Oct '24	404
406		Receipt At site	7 days	14 Oct '24	23 Oct '24	405
407		**Diaphragm Valves**	**155.63 days**	**20 Mar '24**	**23 Oct '24**	
408		Release of Enquiry	5 days	20 Mar '24	26 Mar '24	391
409		Receipt of Offers	7 days	27 Mar '24	04 Apr '24	408
410		Technical Clearance for Ordering	5 days	05 Apr '24	11 Apr '24	409
411		Ordering	5 days	12 Apr '24	18 Apr '24	410
412		Receipt of Post Order Documents from Vendor	7 days	19 Apr '24	29 Apr '24	411
413		Submission of Documents	5 days	30 Apr '24	06 May '24	412
414		Receipt of 1st comments	10 days	07 May '24	20 May '24	413
415		Re-submission	5 days	21 May '24	27 May '24	414
416		Final Approval	5 days	28 May '24	03 Jun '24	415
417		Manufacturing Clearance	1 day	28 May '24	28 May '24	415
418		Manufacturing	120 days	28 May '24	30 Sep '24	417
419		Inspection & Dispatch Clearance	10 days	30 Sep '24	14 Oct '24	418
420		Receipt At site	7 days	14 Oct '24	23 Oct '24	419
421		**Ball Valves**	**155.63 days**	**20 Mar '24**	**23 Oct '24**	
422		Release of Enquiry	5 days	20 Mar '24	26 Mar '24	391
423		Receipt of Offers	7 days	27 Mar '24	04 Apr '24	422
424		Technical Clearance for Ordering	5 days	05 Apr '24	11 Apr '24	423
425		Ordering	5 days	12 Apr '24	18 Apr '24	424
426		Receipt of Post Order Documents from Vendor	7 days	19 Apr '24	29 Apr '24	425
427		Submission of Documents	5 days	30 Apr '24	06 May '24	426
428		Receipt of 1st comments	10 days	07 May '24	20 May '24	427
429		Re-submission	5 days	21 May '24	27 May '24	428
430		Final Approval	5 days	28 May '24	03 Jun '24	429
431		Manufacturing Clearance	1 day	28 May '24	28 May '24	429
432		Manufacturing	120 days	28 May '24	30 Sep '24	431
433		Inspection & Dispatch Clearance	10 days	30 Sep '24	14 Oct '24	432
434		Receipt At site	7 days	14 Oct '24	23 Oct '24	433
435		**Gate Valves**	**155.63 days**	**20 Mar '24**	**23 Oct '24**	
436		Release of Enquiry	5 days	20 Mar '24	26 Mar '24	391
437		Receipt of Offers	7 days	27 Mar '24	04 Apr '24	436
438		Technical Clearance for Ordering	5 days	05 Apr '24	11 Apr '24	437
439		Ordering	5 days	12 Apr '24	18 Apr '24	438
440		Receipt of Post Order Documents from Vendor	7 days	19 Apr '24	29 Apr '24	439

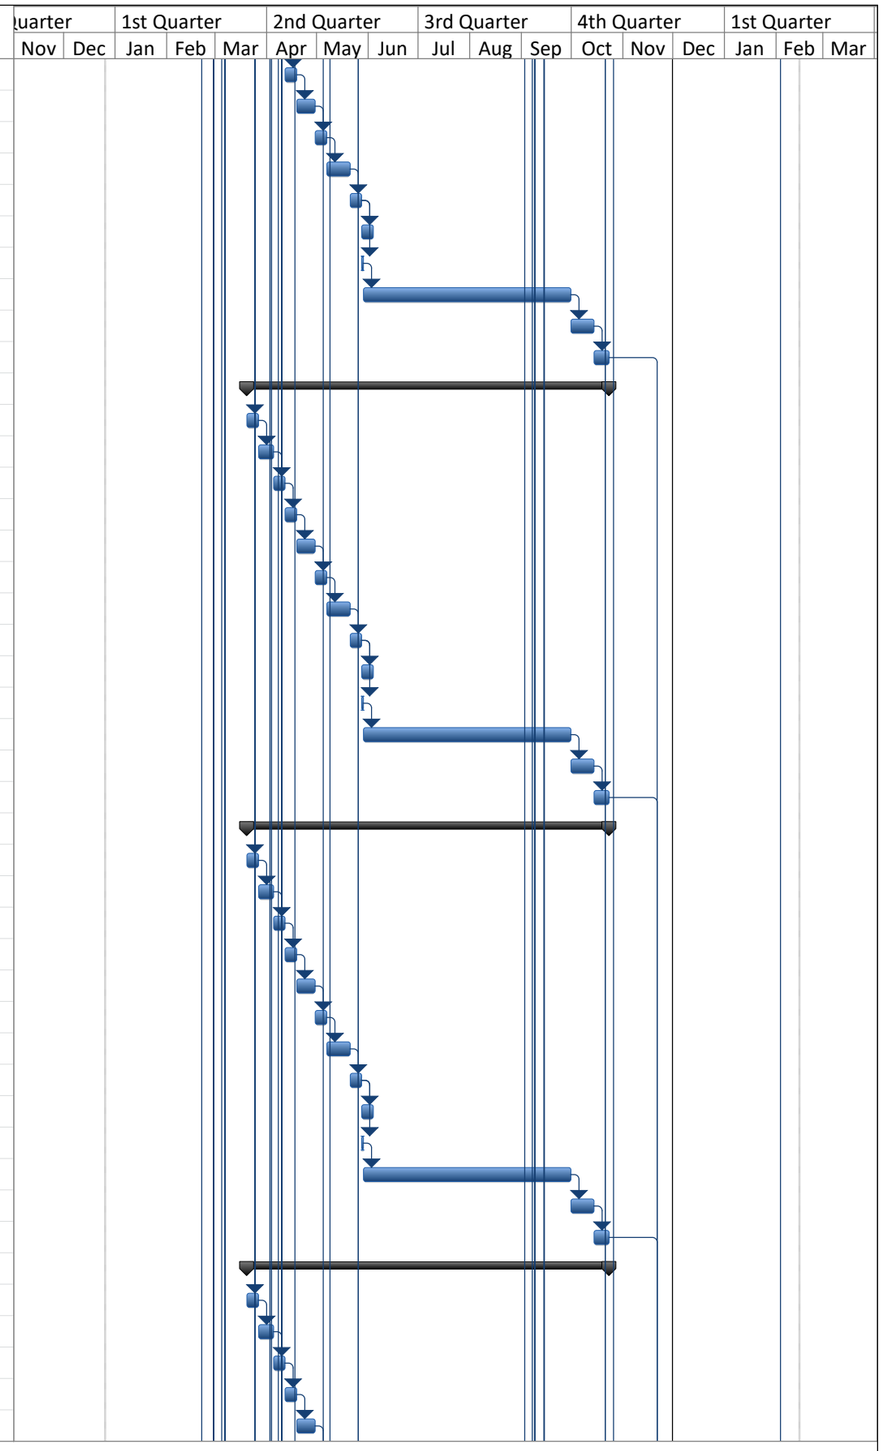

200 m3/hr DM RO Chain at RIL HMD
Start Date: 23.12.26

Task		Project Summary		Inactive Milestone		Manual Summary Rollup		Deadline	
Split		External Tasks		Inactive Summary		Manual Summary		Progress	
Milestone		External Milestone		Manual Task		Start-only			
Summary		Inactive Task		Duration-only		Finish-only			

ID	Task Name	Duration	Start	Finish	Predecessors
441	Submission of Documents	5 days	30 Apr '24	06 May '24	440
442	Receipt of 1st comments	10 days	07 May '24	20 May '24	441
443	Re-submission	5 days	21 May '24	27 May '24	442
444	Final Approval	5 days	28 May '24	03 Jun '24	443
445	Manufacturing Clearance	1 day	28 May '24	28 May '24	443
446	Manufacturing	120 days	28 May '24	30 Sep '24	445
447	Inspection & Dispatch Clearance	10 days	30 Sep '24	14 Oct '24	446
448	Receipt At site	7 days	14 Oct '24	23 Oct '24	447
449	**Globe Valves**	**155.63 days**	**20 Mar '24**	**23 Oct '24**	
450	Release of Enquiry	5 days	20 Mar '24	26 Mar '24	391
451	Receipt of Offers	7 days	27 Mar '24	04 Apr '24	450
452	Technical Clearance for Ordering	5 days	05 Apr '24	11 Apr '24	451
453	Ordering	5 days	12 Apr '24	18 Apr '24	452
454	Receipt of Post Order Documents from Vendor	7 days	19 Apr '24	29 Apr '24	453
455	Submission of Documents	5 days	30 Apr '24	06 May '24	454
456	Receipt of 1st comments	10 days	07 May '24	20 May '24	455
457	Re-submission	5 days	21 May '24	27 May '24	456
458	Final Approval	5 days	28 May '24	03 Jun '24	457
459	Manufacturing Clearance	1 day	28 May '24	28 May '24	457
460	Manufacturing	120 days	28 May '24	30 Sep '24	459
461	Inspection & Dispatch Clearance	10 days	30 Sep '24	14 Oct '24	460
462	Receipt At site	7 days	14 Oct '24	23 Oct '24	461
463	**Check Valves**	**155.63 days**	**20 Mar '24**	**23 Oct '24**	
464	Release of Enquiry	5 days	20 Mar '24	26 Mar '24	391
465	Receipt of Offers	7 days	27 Mar '24	04 Apr '24	464
466	Technical Clearance for Ordering	5 days	05 Apr '24	11 Apr '24	465
467	Ordering	5 days	12 Apr '24	18 Apr '24	466
468	Receipt of Post Order Documents from Vendor	7 days	19 Apr '24	29 Apr '24	467
469	Submission of Documents	5 days	30 Apr '24	06 May '24	468
470	Receipt of 1st comments	10 days	07 May '24	20 May '24	469
471	Re-submission	5 days	21 May '24	27 May '24	470
472	Final Approval	5 days	28 May '24	03 Jun '24	471
473	Manufacturing Clearance	1 day	28 May '24	28 May '24	471
474	Manufacturing	120 days	28 May '24	30 Sep '24	473
475	Inspection & Dispatch Clearance	10 days	30 Sep '24	14 Oct '24	474
476	Receipt At site	7 days	14 Oct '24	23 Oct '24	475
477	**Non-Metallic Valves**	**140.88 days**	**20 Mar '24**	**02 Oct '24**	
478	Release of Enquiry	5 days	20 Mar '24	26 Mar '24	391
479	Receipt of Offers	7 days	27 Mar '24	04 Apr '24	478
480	Technical Clearance for Ordering	5 days	05 Apr '24	11 Apr '24	479
481	Ordering	5 days	12 Apr '24	18 Apr '24	480
482	Receipt of Post Order Documents from Vendor	7 days	19 Apr '24	29 Apr '24	481
483	Submission of Documents	5 days	30 Apr '24	06 May '24	482
484	Receipt of 1st comments	10 days	07 May '24	20 May '24	483

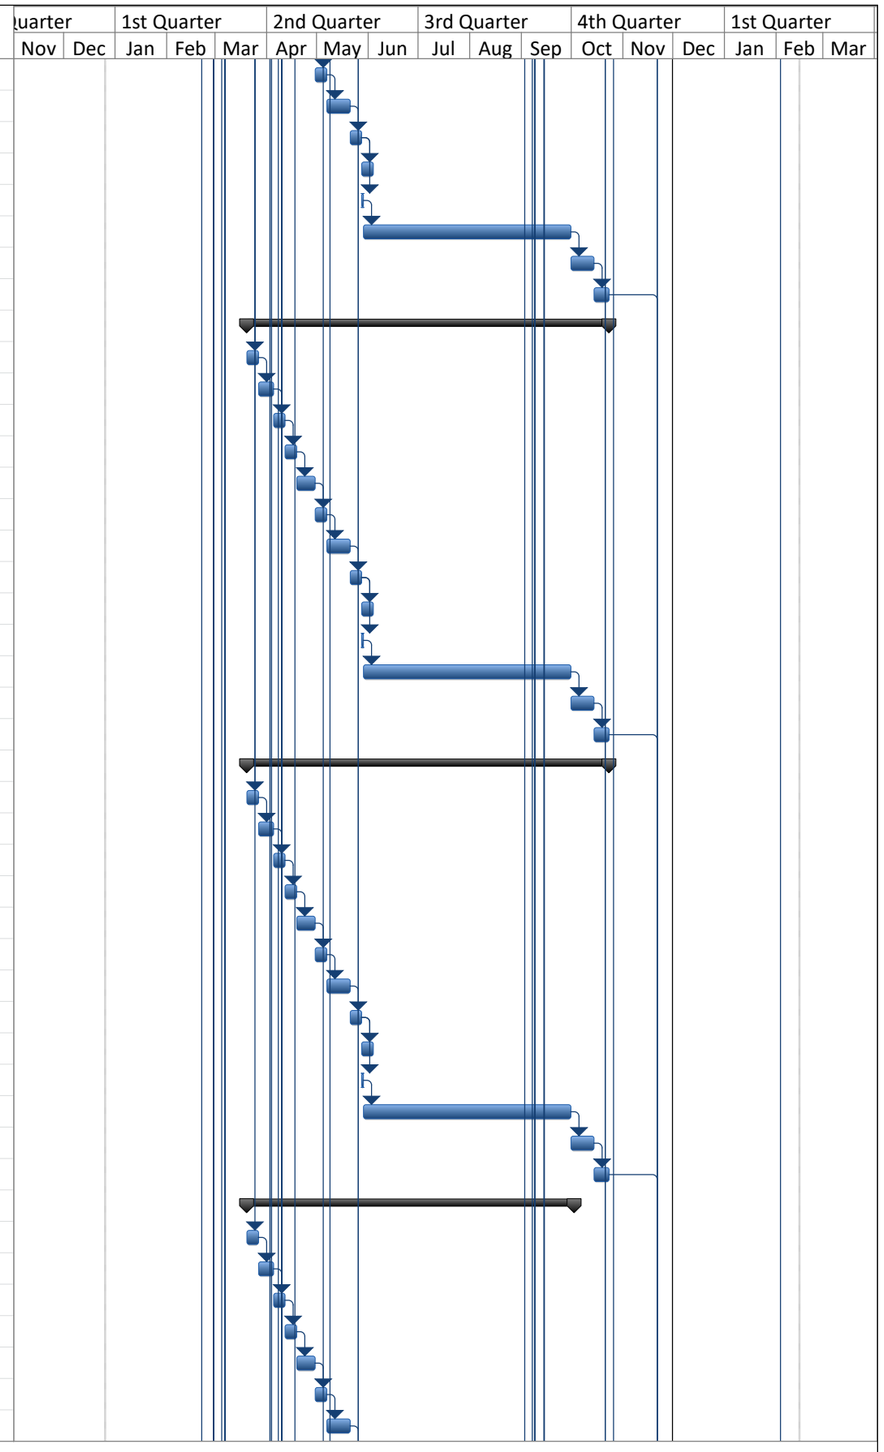

200 m3/hr DM RO Chain at RIL HMD
Start Date: 23.12.26

Task		Project Summary		Inactive Milestone		Manual Summary Rollup		Deadline	
Split		External Tasks		Inactive Summary		Manual Summary		Progress	
Milestone		External Milestone		Manual Task		Start-only			
Summary		Inactive Task		Duration-only		Finish-only			

ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors
485		Re-submission	5 days	21 May '24	27 May '24	484
486		Final Approval	5 days	28 May '24	03 Jun '24	485
487		Manufacturing Clearance	1 day	28 May '24	28 May '24	485
488		Manufacturing	100 days	28 May '24	09 Sep '24	487
489		Inspection & Dispatch Clearance	10 days	09 Sep '24	23 Sep '24	488
490		Receipt At site	7 days	23 Sep '24	02 Oct '24	489
491		**Motorized Barrel Pumps**	**140.88 days**	**26 Feb '24**	**09 Sep '24**	
492		Release of Enquiry	5 days	26 Feb '24	01 Mar '24	17,22
493		Receipt of Offers	7 days	04 Mar '24	12 Mar '24	492
494		Technical Clearance for Ordering	5 days	13 Mar '24	19 Mar '24	493
495		Ordering	5 days	20 Mar '24	26 Mar '24	494
496		Receipt of Post Order Documents from Vendor	7 days	27 Mar '24	04 Apr '24	495
497		Submission of Documents	5 days	05 Apr '24	11 Apr '24	496
498		Receipt of 1st comments	10 days	12 Apr '24	25 Apr '24	497
499		Re-submission	5 days	26 Apr '24	02 May '24	498
500		Final Approval	5 days	03 May '24	09 May '24	499
501		Manufacturing Clearance	1 day	03 May '24	03 May '24	499
502		Manufacturing	100 days	03 May '24	15 Aug '24	501
503		Inspection & Dispatch Clearance	10 days	15 Aug '24	29 Aug '24	502
504		Receipt At site	7 days	29 Aug '24	09 Sep '24	503
505		**Piping**	**198.75 days**	**19 Feb '24**	**21 Nov '24**	
506		Submission of Piping Specifications	7 days	19 Feb '24	27 Feb '24	16
507		Receipt of 1st comments	10 days	28 Feb '24	12 Mar '24	506
508		Re-submission	5 days	13 Mar '24	19 Mar '24	507
509		Final Approval	5 days	20 Mar '24	26 Mar '24	508
510		3D Model	20 days	26 Feb '24	22 Mar '24	53
511		30% Model review	2 days	25 Mar '24	26 Mar '24	510
512		30% Model closure report	10 days	27 Mar '24	09 Apr '24	511
513		60% Model review	2 days	22 May '24	23 May '24	512FS+30 days
514		60% Model closure report	10 days	24 May '24	06 Jun '24	513
515		90% Model review	2 days	05 Jul '24	08 Jul '24	514FS+20 days
516		90% Model closure report	10 days	09 Jul '24	22 Jul '24	515
517		Submission of final Model	7 days	23 Jul '24	31 Jul '24	516
518		Release of piping isometric- SS	7 days	07 Jun '24	17 Jun '24	514
519		Release of piping isometric- CS/CSRL	7 days	18 Jun '24	26 Jun '24	518
520		Release of piping isometric-Non Metallic	7 days	27 Jun '24	05 Jul '24	519
521		Release of BOM for Piping Raw material	5 days	18 Jun '24	24 Jun '24	518
522		Receipt of Offers	7 days	25 Jun '24	03 Jul '24	521
523		Ordering	5 days	04 Jul '24	10 Jul '24	522
524		Receipt of Material at Piping Fabricators' Shop	30 days	11 Jul '24	21 Aug '24	523
525		Release of Order & Clearance for fabrication of spools-SS/CS/CSRL	1 day	22 Aug '24	22 Aug '24	524
526		Fabrication	65 days	22 Aug '24	29 Oct '24	525
527		Inspection & Dispatch Clearance	10 days	29 Oct '24	12 Nov '24	526

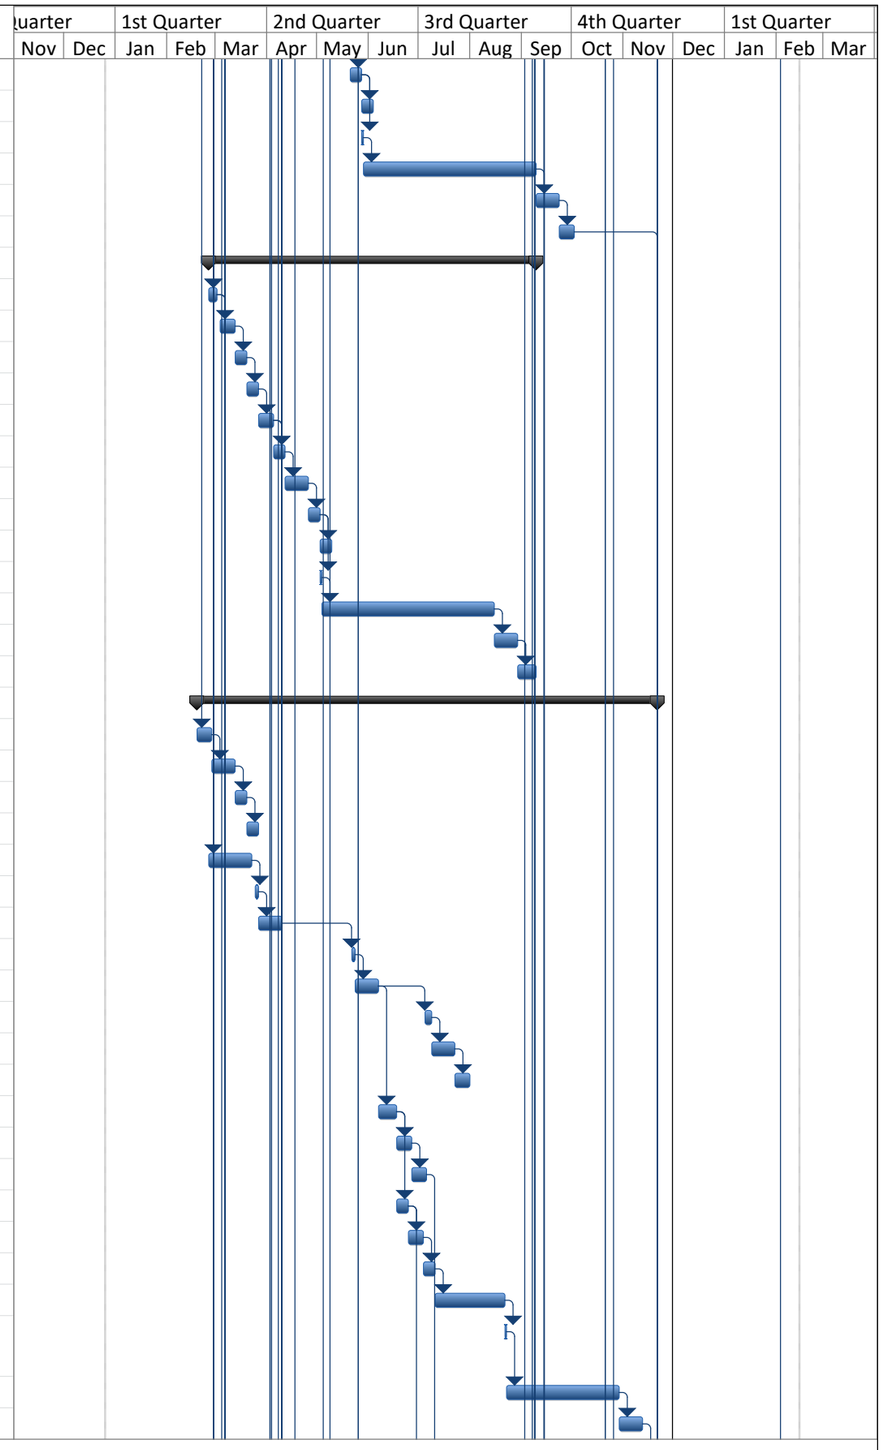

200 m3/hr DM RO Chain at RIL HMD
Start Date: 23.12.26

Task		Project Summary		Inactive Milestone		Manual Summary Rollup		Deadline	
Split		External Tasks		Inactive Summary		Manual Summary		Progress	
Milestone		External Milestone		Manual Task		Start-only			
Summary		Inactive Task		Duration-only		Finish-only			

ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors
528		Receipt At site	7 days	12 Nov '24	21 Nov '24	527
529		**Pipe Supports**	**75 days**	**08 Jul '24**	**18 Oct '24**	
530		Release of Pipe support GA	7 days	08 Jul '24	16 Jul '24	520
531		Receipt of 1st comments	10 days	17 Jul '24	30 Jul '24	530
532		Re-submission	5 days	31 Jul '24	06 Aug '24	531
533		Final Approval	5 days	07 Aug '24	13 Aug '24	532
534		Release of Order & Clearance for fabrication of Pipe supports	1 day	17 Jul '24	17 Jul '24	530
535		Fabrication	50 days	18 Jul '24	25 Sep '24	534
536		Inspection & Dispatch Clearance	10 days	26 Sep '24	09 Oct '24	535
537		Receipt At site	7 days	10 Oct '24	18 Oct '24	536
538		**Hardware & Gaskets**	**51 days**	**25 Jun '24**	**03 Sep '24**	
539		Release of BOM	5 days	25 Jun '24	01 Jul '24	521
540		Ordering & Clearance for Manufacturing	7 days	02 Jul '24	10 Jul '24	539
541		Manufacturing	30 days	10 Jul '24	10 Aug '24	540
542		Inspection & Dispatch Clearance	10 days	12 Aug '24	23 Aug '24	541
543		Receipt At site	7 days	26 Aug '24	03 Sep '24	542
544		**Air Grid**	**89 days**	**30 Apr '24**	**30 Aug '24**	
545		Release of Fabrication Drawing	7 days	30 Apr '24	08 May '24	76
546		Receipt of Offers	7 days	09 May '24	17 May '24	545
547		Technical Clearance for Ordering	1 day	20 May '24	20 May '24	546
548		Ordering & Clearance for Fabrication	7 days	21 May '24	29 May '24	547
549		Fabrication	50 days	30 May '24	07 Aug '24	548
550		Inspection & Dispatch Clearance	10 days	08 Aug '24	21 Aug '24	549
551		Receipt At site	7 days	22 Aug '24	30 Aug '24	550
552		Completion of Mechanical Engineering & Procurement	0 days	21 Nov '24	21 Nov '24	113
553		**Electrical Engineering & Procurement**	**208.88 days**	**26 Feb '24**	**12 Dec '24**	
554		Release of Prelimenary Load List	1 day	04 Mar '24	04 Mar '24	207,277,291,305,319,333,3
555		Submission of Electrical Load List	2 days	05 Apr '24	08 Apr '24	211,281,295,309,323,337,3
556		Receipt of 1st comments	10 days	09 Apr '24	22 Apr '24	555
557		Re-submission	5 days	23 Apr '24	29 Apr '24	556
558		Final Approval	5 days	30 Apr '24	06 May '24	557
559		**LT Motors**	**156 days**	**05 Mar '24**	**08 Oct '24**	
560		Release of Enquiry	5 days	05 Mar '24	11 Mar '24	554
561		Receipt of Offers	7 days	12 Mar '24	20 Mar '24	560
562		Technical Clearance for Ordering	5 days	21 Mar '24	27 Mar '24	561
563		Ordering	5 days	28 Mar '24	03 Apr '24	562
564		Receipt of Post Order Documents from Vendor	7 days	04 Apr '24	12 Apr '24	563
565		Submission of Documents	5 days	15 Apr '24	19 Apr '24	564
566		Receipt of 1st comments	10 days	22 Apr '24	03 May '24	565
567		Re-submission	5 days	06 May '24	10 May '24	566
568		Final Approval	5 days	13 May '24	17 May '24	567
569		Manufacturing Clearance	1 day	13 May '24	13 May '24	567

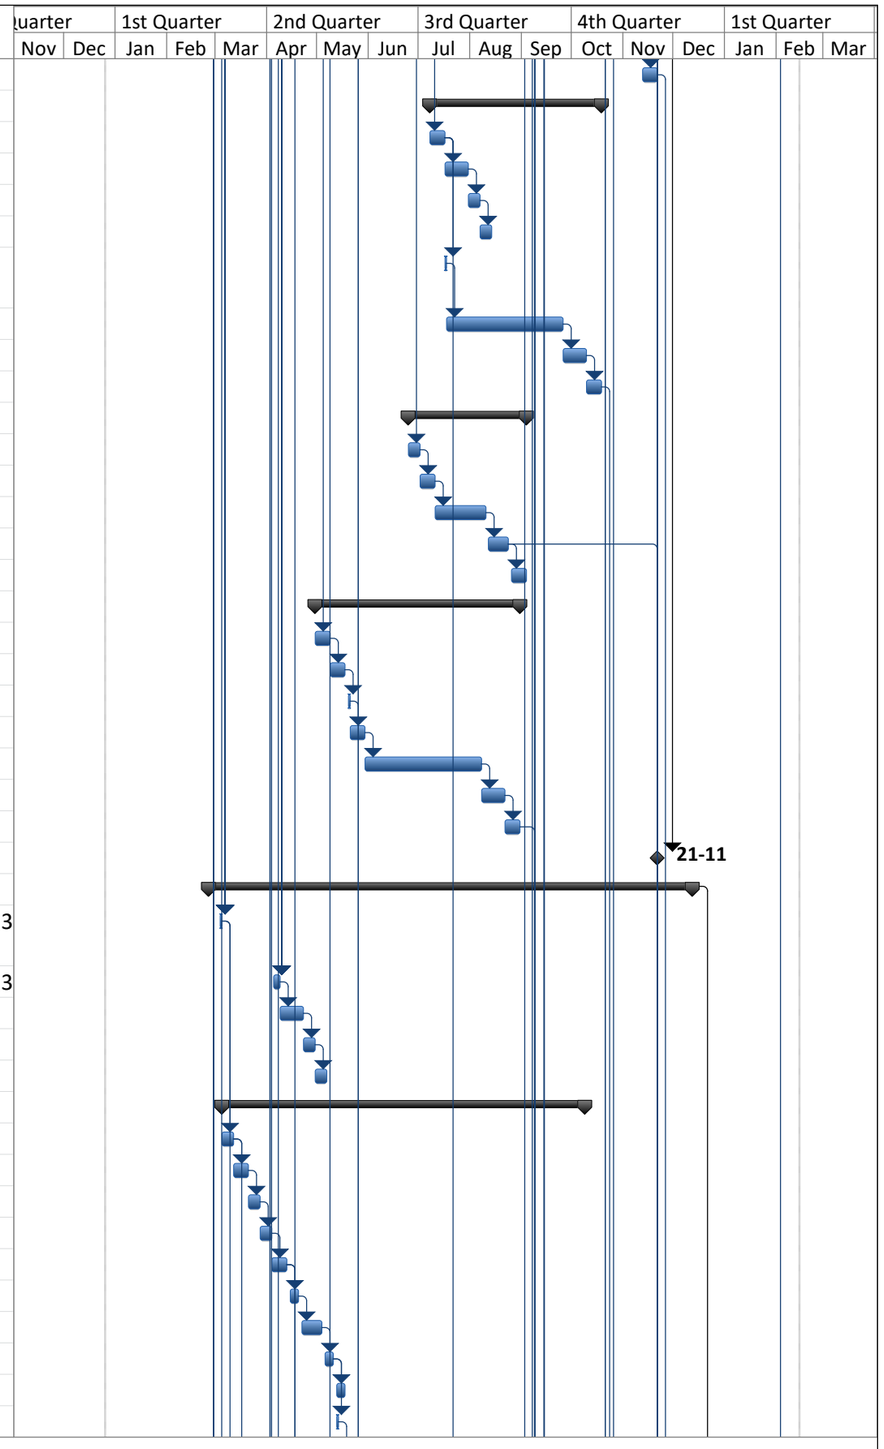

200 m3/hr DM RO Chain at RIL HMD
Start Date: 23.12.26

Task		Project Summary		Inactive Milestone		Manual Summary Rollup		Deadline	
Split		External Tasks		Inactive Summary		Manual Summary		Progress	
Milestone		External Milestone		Manual Task		Start-only			
Summary		Inactive Task		Duration-only		Finish-only			

ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors
570		Manufacturing	120 days	13 May '24	14 Sep '24	569
571		Inspection & Dispatch Clearance	10 days	16 Sep '24	27 Sep '24	570
572		Receipt At site	7 days	30 Sep '24	08 Oct '24	571
573		**Earthing Material**	**72 days**	**26 Feb '24**	**04 Jun '24**	
574		Submission of Earthing Calculations & Layout	7 days	26 Feb '24	05 Mar '24	53
575		Receipt of 1st comments	10 days	06 Mar '24	19 Mar '24	574
576		Re-submission	5 days	20 Mar '24	26 Mar '24	575
577		Final Approval	5 days	27 Mar '24	02 Apr '24	576
578		Release of Enquiry	3 days	06 Mar '24	08 Mar '24	574
579		Receipt of Offers	5 days	11 Mar '24	15 Mar '24	578
580		Ordering & Manufacturing Clearance	7 days	18 Mar '24	26 Mar '24	579
581		Manufacturing	45 days	26 Mar '24	11 May '24	580
582		Inspection & Dispatch Clearance	10 days	13 May '24	24 May '24	581
583		Receipt At site	7 days	27 May '24	04 Jun '24	582
584		**VFD Panel**	**162.63 days**	**15 Apr '24**	**27 Nov '24**	
585		VFD Control Scheme	7 days	15 Apr '24	23 Apr '24	564
586		Release of Enquiry	5 days	24 Apr '24	30 Apr '24	585
587		Receipt of Offers	7 days	01 May '24	09 May '24	586
588		Technical Clearance for Ordering	5 days	10 May '24	16 May '24	587
589		Ordering	5 days	17 May '24	23 May '24	588
590		Receipt of Post Order Documents from Vendor	7 days	24 May '24	03 Jun '24	589
591		Submission of Documents	5 days	04 Jun '24	10 Jun '24	590
592		Receipt of 1st comments	10 days	11 Jun '24	24 Jun '24	591
593		Re-submission	5 days	25 Jun '24	01 Jul '24	592
594		Final Approval	5 days	02 Jul '24	08 Jul '24	593
595		Manufacturing Clearance	1 day	02 Jul '24	02 Jul '24	593
596		Manufacturing	120 days	02 Jul '24	04 Nov '24	595
597		Inspection & Dispatch Clearance	10 days	04 Nov '24	18 Nov '24	596
598		Receipt At site	7 days	18 Nov '24	27 Nov '24	597
599		**LCS**	**134 days**	**12 Mar '24**	**13 Sep '24**	
600		Release of Enquiry	5 days	12 Mar '24	18 Mar '24	560
601		Receipt of Offers	7 days	19 Mar '24	27 Mar '24	600
602		Technical Clearance for Ordering	5 days	28 Mar '24	03 Apr '24	601
603		Ordering	5 days	04 Apr '24	10 Apr '24	602
604		Receipt of Post Order Documents from Vendor	7 days	11 Apr '24	19 Apr '24	603
605		Submission of Documents	5 days	22 Apr '24	26 Apr '24	604
606		Receipt of 1st comments	10 days	29 Apr '24	10 May '24	605
607		Re-submission	5 days	13 May '24	17 May '24	606
608		Final Approval	5 days	20 May '24	24 May '24	607
609		Manufacturing Clearance	1 day	20 May '24	20 May '24	607
610		Manufacturing	90 days	20 May '24	21 Aug '24	609
611		Inspection & Dispatch Clearance	10 days	22 Aug '24	04 Sep '24	610
612		Receipt At site	7 days	05 Sep '24	13 Sep '24	611
613		**Power & Control Cables**	**147.88 days**	**05 Mar '24**	**26 Sep '24**	

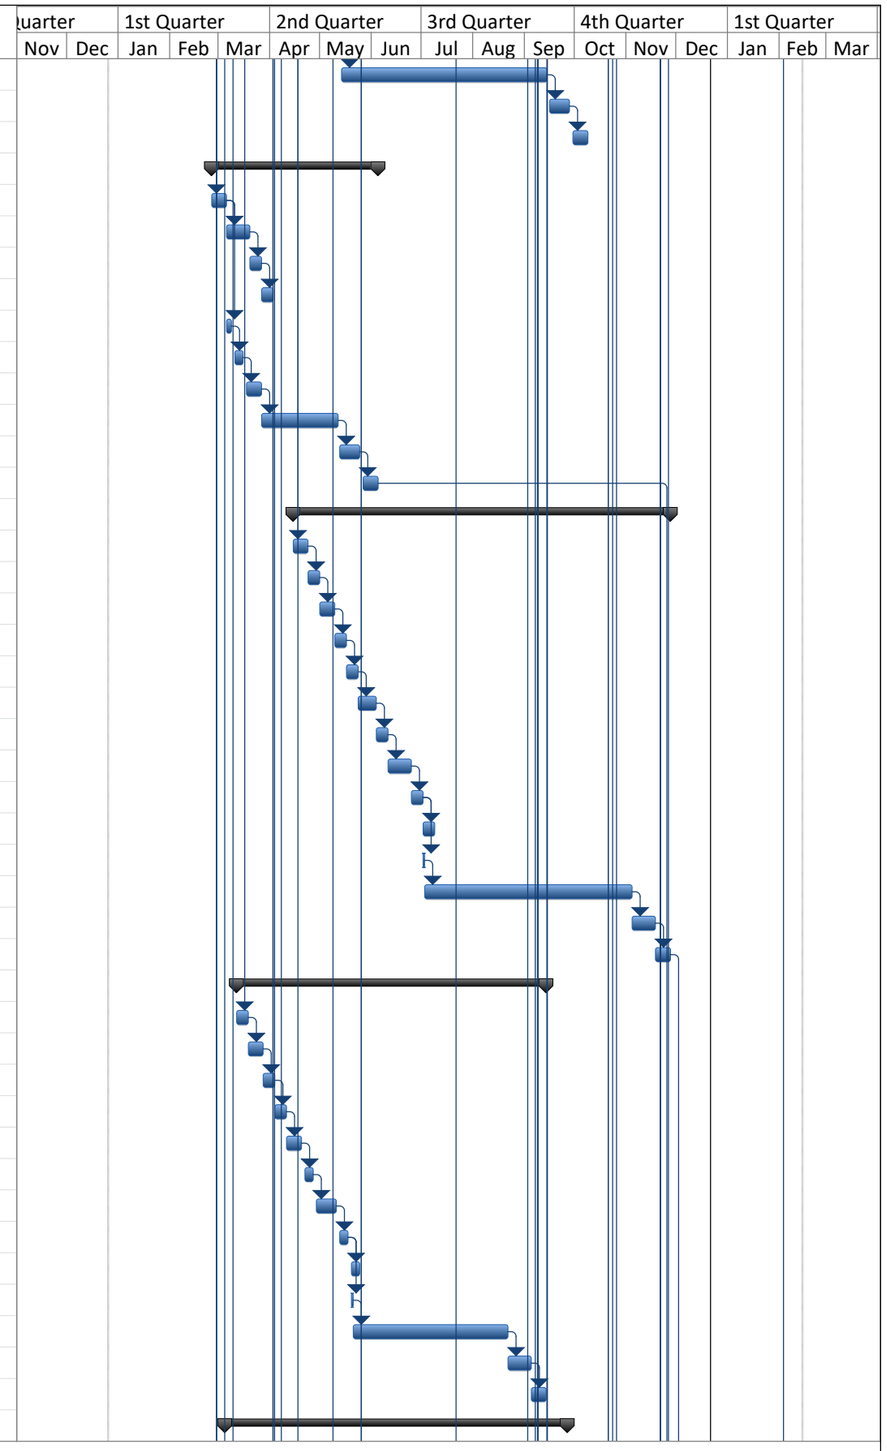

200 m3/hr DM RO Chain at RIL HMD
Start Date: 23.12.26

Task		Project Summary		Inactive Milestone		Manual Summary Rollup		Deadline	
Split		External Tasks		Inactive Summary		Manual Summary		Progress	
Milestone		External Milestone		Manual Task		Start-only			
Summary		Inactive Task		Duration-only		Finish-only			

ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors
614		Submission of Cable Schedule	7 days	05 Mar '24	13 Mar '24	53,554
615		Receipt of 1st comments	10 days	14 Mar '24	27 Mar '24	614
616		Re-submission	5 days	28 Mar '24	03 Apr '24	615
617		Final Approval	5 days	04 Apr '24	10 Apr '24	616
618		Release of Enquiry	5 days	14 Mar '24	20 Mar '24	614
619		Receipt of Offers	7 days	21 Mar '24	29 Mar '24	618
620		Technical Clearance for Ordering	5 days	01 Apr '24	05 Apr '24	619
621		Ordering	5 days	08 Apr '24	12 Apr '24	620
622		Receipt of Post Order Documents from Vendor	7 days	15 Apr '24	23 Apr '24	621
623		Submission of Documents	5 days	24 Apr '24	30 Apr '24	622
624		Receipt of 1st comments	10 days	01 May '24	14 May '24	623
625		Re-submission	5 days	15 May '24	21 May '24	624
626		Final Approval	5 days	22 May '24	28 May '24	625
627		Manufacturing Clearance	1 day	22 May '24	22 May '24	625
628		Manufacturing	100 days	22 May '24	03 Sep '24	627
629		Inspection & Dispatch Clearance	10 days	03 Sep '24	17 Sep '24	628
630		Receipt At site	7 days	17 Sep '24	26 Sep '24	629
631		**Cable Trays & Accessories**	**164 days**	**04 Apr '24**	**19 Nov '24**	
632		Submission of Cable Tray Layout	10 days	04 Apr '24	17 Apr '24	53,616,788
633		Receipt of 1st comments	10 days	18 Apr '24	01 May '24	632
634		Re-submission	5 days	02 May '24	08 May '24	633
635		Final Approval	5 days	09 May '24	15 May '24	634
636		Release of Enquiry	5 days	16 May '24	22 May '24	635
637		Receipt of Offers	7 days	23 May '24	31 May '24	636
638		Technical Clearance for Ordering	5 days	03 Jun '24	07 Jun '24	637
639		Ordering	5 days	10 Jun '24	14 Jun '24	638
640		Receipt of Post Order Documents from Vendor	7 days	17 Jun '24	25 Jun '24	639
641		Submission of Documents	5 days	26 Jun '24	02 Jul '24	640
642		Receipt of 1st comments	10 days	03 Jul '24	16 Jul '24	641
643		Re-submission	5 days	17 Jul '24	23 Jul '24	642
644		Final Approval	5 days	24 Jul '24	30 Jul '24	643
645		Manufacturing Clearance	1 day	24 Jul '24	24 Jul '24	643
646		Manufacturing	90 days	24 Jul '24	25 Oct '24	645
647		Inspection & Dispatch Clearance	10 days	28 Oct '24	08 Nov '24	646
648		Receipt At site	7 days	11 Nov '24	19 Nov '24	647
649		**Cable Tray Support Material**	**96 days**	**17 Jul '24**	**27 Nov '24**	
650		Release of Cable Tray support GA	7 days	17 Jul '24	25 Jul '24	632,530
651		Receipt of 1st comments	10 days	26 Jul '24	08 Aug '24	650
652		Re-submission	5 days	09 Aug '24	15 Aug '24	651
653		Final Approval	5 days	16 Aug '24	22 Aug '24	652
654		Release of Order & Clearance for fabrication of Pipe supports	7 days	23 Aug '24	02 Sep '24	653
655		Fabrication	45 days	03 Sep '24	04 Nov '24	654
656		Inspection & Dispatch Clearance	10 days	05 Nov '24	18 Nov '24	655

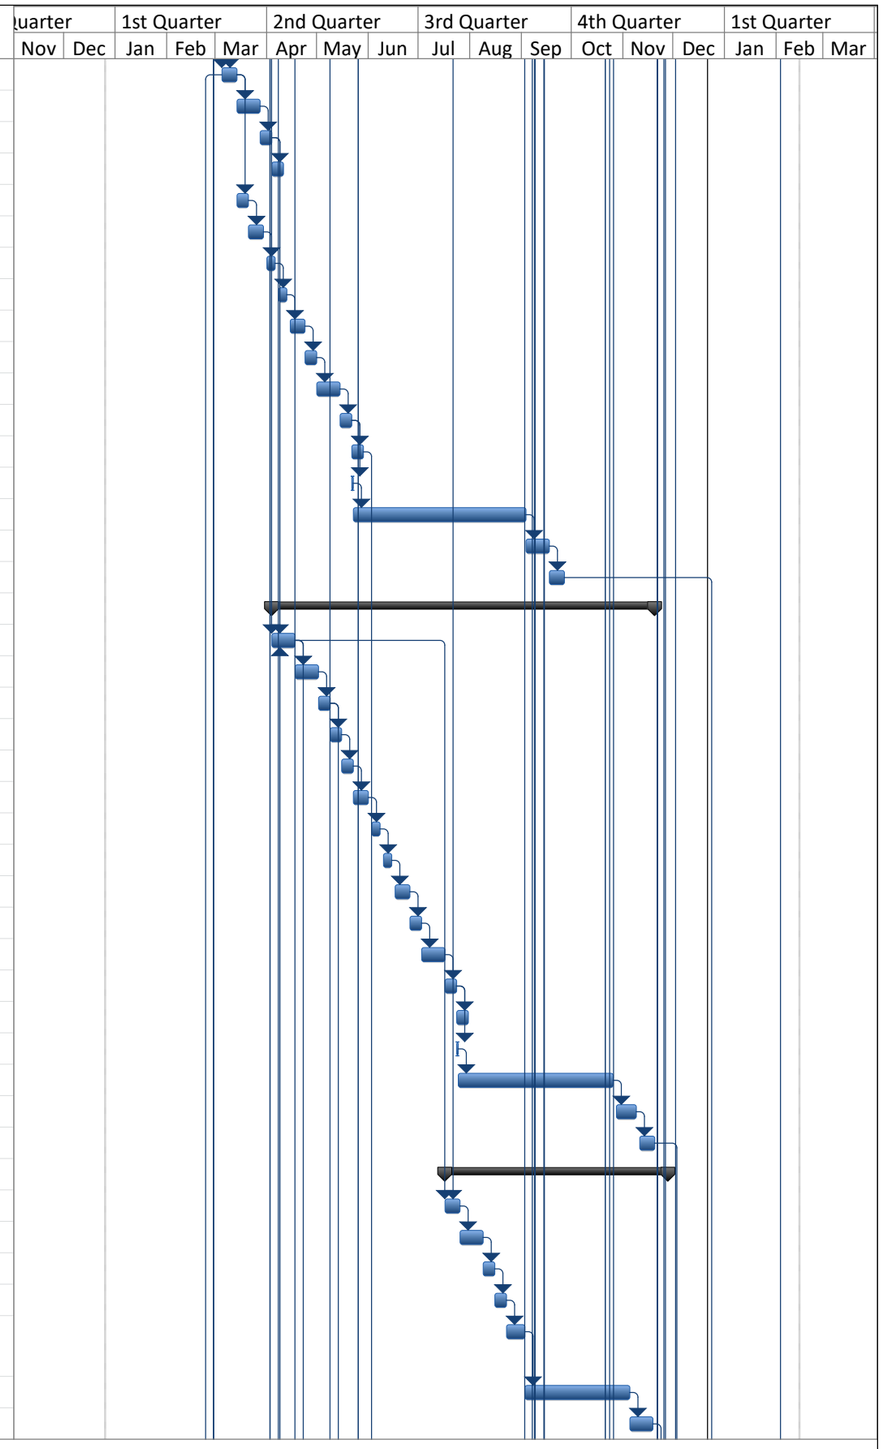

200 m3/hr DM RO Chain at RIL HMD
Start Date: 23.12.26

Task		Project Summary		Inactive Milestone		Manual Summary Rollup		Deadline	
Split		External Tasks		Inactive Summary		Manual Summary		Progress	
Milestone		External Milestone		Manual Task		Start-only			
Summary		Inactive Task		Duration-only		Finish-only			

ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors
657		Receipt At site	7 days	19 Nov '24	27 Nov '24	656
658		**Cable Glands (Electrical)**	**76.25 days**	**29 May '24**	**12 Sep '24**	
659		Release of BOM	5 days	29 May '24	04 Jun '24	626
660		Receipt of Offers	5 days	05 Jun '24	11 Jun '24	659
661		Ordering & Manufacturing Clearance	5 days	12 Jun '24	18 Jun '24	660
662		Manufacturing	60 days	18 Jun '24	20 Aug '24	661
663		Inspection & Dispatch Clearance	10 days	20 Aug '24	03 Sep '24	662
664		Receipt At site	7 days	03 Sep '24	12 Sep '24	663
665		**Lighting Material**	**170.88 days**	**18 Apr '24**	**12 Dec '24**	
666		Submission of Lighting Calculations & Layout	10 days	18 Apr '24	01 May '24	53,632
667		Receipt of 1st comments	10 days	02 May '24	15 May '24	666
668		Re-submission	5 days	16 May '24	22 May '24	667
669		Final Approval	5 days	23 May '24	29 May '24	668
670		Release of Enquiry	5 days	30 May '24	05 Jun '24	669
671		Receipt of Offers	7 days	06 Jun '24	14 Jun '24	670
672		Technical Clearance for Ordering	5 days	17 Jun '24	21 Jun '24	671
673		Ordering	5 days	24 Jun '24	28 Jun '24	672
674		Receipt of Post Order Documents from Vendor	7 days	01 Jul '24	09 Jul '24	673
675		Submission of Documents	5 days	10 Jul '24	16 Jul '24	674
676		Receipt of 1st comments	10 days	17 Jul '24	30 Jul '24	675
677		Re-submission	5 days	31 Jul '24	06 Aug '24	676
678		Final Approval	5 days	07 Aug '24	13 Aug '24	677
679		Manufacturing Clearance	1 day	07 Aug '24	07 Aug '24	677
680		Manufacturing	100 days	07 Aug '24	19 Nov '24	679
681		Inspection & Dispatch Clearance	10 days	19 Nov '24	03 Dec '24	680
682		Receipt At site	7 days	03 Dec '24	12 Dec '24	681
683		Completion of Electrical Engineering & Procurement	0 days	12 Dec '24	12 Dec '24	553
684		**Instrumentation Engineering & Procurement**	**246 days**	**26 Dec '23**	**03 Dec '24**	
685		Submission of Instrument Index	7 days	26 Feb '24	05 Mar '24	17,22
686		Receipt of 1st comments	10 days	06 Mar '24	19 Mar '24	685
687		Re-submission	5 days	20 Mar '24	26 Mar '24	686
688		Final Approval	5 days	27 Mar '24	02 Apr '24	687
689		**Pressure & Differential Pressure Gauges**	**148.75 days**	**27 Mar '24**	**21 Oct '24**	
690		Release of Enquiry	5 days	27 Mar '24	02 Apr '24	687
691		Receipt of Offers	7 days	03 Apr '24	11 Apr '24	690
692		Technical Clearance for Ordering	5 days	12 Apr '24	18 Apr '24	691
693		Ordering	5 days	19 Apr '24	25 Apr '24	692
694		Receipt of Post Order Documents from Vendor	7 days	26 Apr '24	06 May '24	693
695		Submission of Documents	5 days	07 May '24	13 May '24	694
696		Receipt of 1st comments	10 days	14 May '24	27 May '24	695
697		Re-submission	5 days	28 May '24	03 Jun '24	696
698		Final Approval	5 days	04 Jun '24	10 Jun '24	697
699		Manufacturing Clearance	1 day	04 Jun '24	04 Jun '24	697
700		Manufacturing	110 days	04 Jun '24	26 Sep '24	699

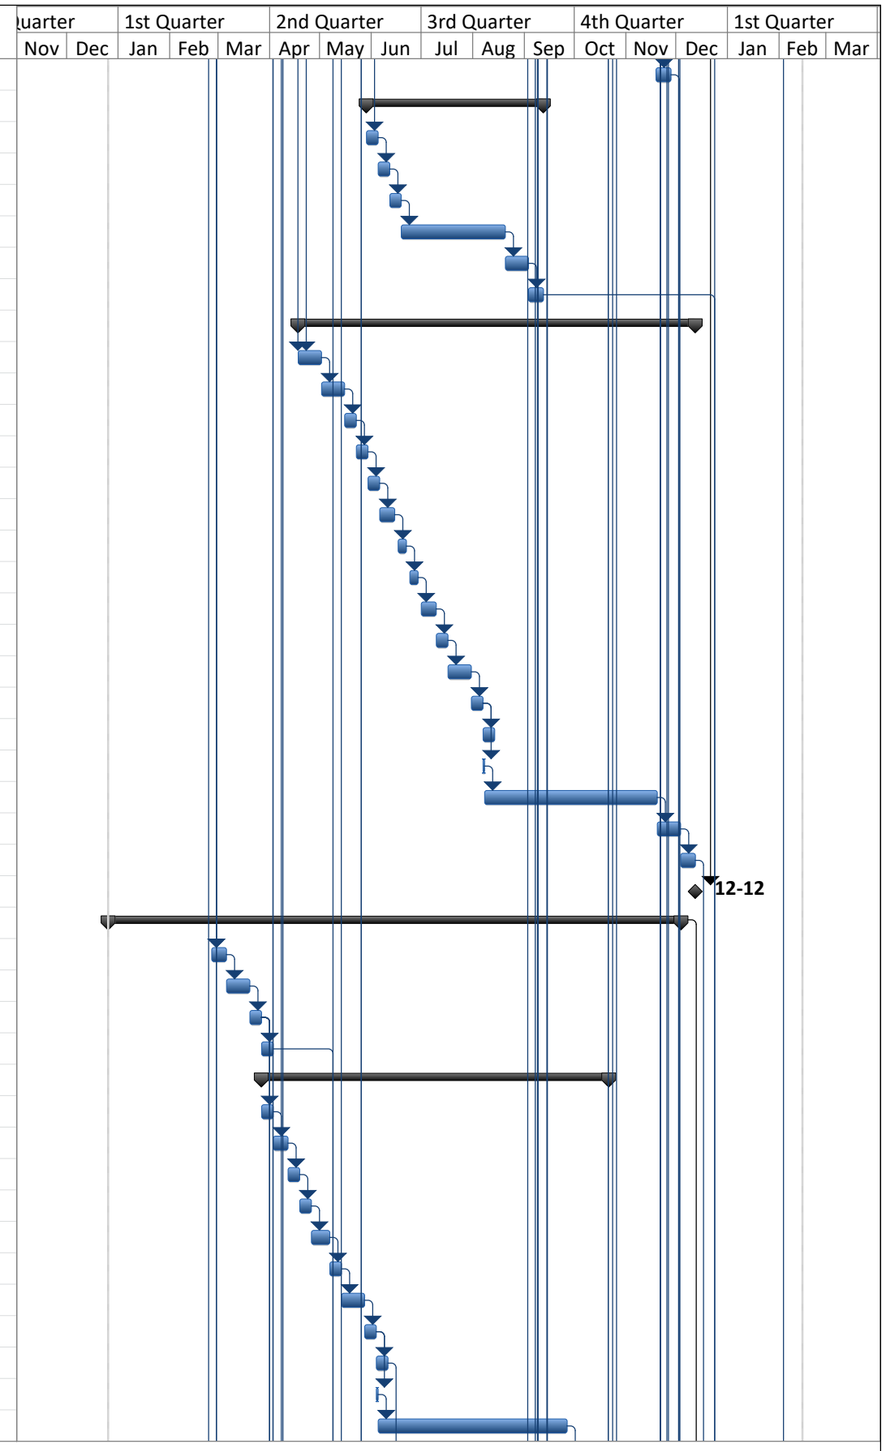

200 m3/hr DM RO Chain at RIL HMD
Start Date: 23.12.26

Task		Project Summary		Inactive Milestone		Manual Summary Rollup		Deadline	
Split		External Tasks		Inactive Summary		Manual Summary		Progress	
Milestone		External Milestone		Manual Task		Start-only			
Summary		Inactive Task		Duration-only		Finish-only			

ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors
701		Inspection & Dispatch Clearance	10 days	26 Sep '24	10 Oct '24	700
702		Receipt At site	7 days	10 Oct '24	21 Oct '24	701
703		**Level Gauges & Float and Board Level Indicators**	**148.75 days**	**27 Mar '24**	**21 Oct '24**	
704		Release of Enquiry	5 days	27 Mar '24	02 Apr '24	687
705		Receipt of Offers	7 days	03 Apr '24	11 Apr '24	704
706		Technical Clearance for Ordering	5 days	12 Apr '24	18 Apr '24	705
707		Ordering	5 days	19 Apr '24	25 Apr '24	706
708		Receipt of Post Order Documents from Vendor	7 days	26 Apr '24	06 May '24	707
709		Submission of Documents	5 days	07 May '24	13 May '24	708
710		Receipt of 1st comments	10 days	14 May '24	27 May '24	709
711		Re-submission	5 days	28 May '24	03 Jun '24	710
712		Final Approval	5 days	04 Jun '24	10 Jun '24	711
713		Manufacturing Clearance	1 day	04 Jun '24	04 Jun '24	711
714		Manufacturing	110 days	04 Jun '24	26 Sep '24	713
715		Inspection & Dispatch Clearance	10 days	26 Sep '24	10 Oct '24	714
716		Receipt At site	7 days	10 Oct '24	21 Oct '24	715
717		**Transmitters**	**163.5 days**	**27 Mar '24**	**11 Nov '24**	
718		Release of Enquiry	5 days	27 Mar '24	02 Apr '24	687
719		Receipt of Offers	7 days	03 Apr '24	11 Apr '24	718
720		Technical Clearance for Ordering	5 days	12 Apr '24	18 Apr '24	719
721		Ordering	5 days	19 Apr '24	25 Apr '24	720
722		Receipt of Post Order Documents from Vendor	7 days	26 Apr '24	06 May '24	721
723		Submission of Documents	5 days	07 May '24	13 May '24	722
724		Receipt of 1st comments	10 days	14 May '24	27 May '24	723
725		Re-submission	5 days	28 May '24	03 Jun '24	724
726		Final Approval	5 days	04 Jun '24	10 Jun '24	725
727		Manufacturing Clearance	1 day	04 Jun '24	04 Jun '24	725
728		Manufacturing	130 days	04 Jun '24	17 Oct '24	727
729		Inspection & Dispatch Clearance	10 days	17 Oct '24	31 Oct '24	728
730		Receipt At site	7 days	31 Oct '24	11 Nov '24	729
731		**Analyzers**	**163.5 days**	**27 Mar '24**	**11 Nov '24**	
732		Release of Enquiry	5 days	27 Mar '24	02 Apr '24	687
733		Receipt of Offers	7 days	03 Apr '24	11 Apr '24	732
734		Technical Clearance for Ordering	5 days	12 Apr '24	18 Apr '24	733
735		Ordering	5 days	19 Apr '24	25 Apr '24	734
736		Receipt of Post Order Documents from Vendor	7 days	26 Apr '24	06 May '24	735
737		Submission of Documents	5 days	07 May '24	13 May '24	736
738		Receipt of 1st comments	10 days	14 May '24	27 May '24	737
739		Re-submission	5 days	28 May '24	03 Jun '24	738
740		Final Approval	5 days	04 Jun '24	10 Jun '24	739
741		Manufacturing Clearance	1 day	04 Jun '24	04 Jun '24	739
742		Manufacturing	130 days	04 Jun '24	17 Oct '24	741
743		Inspection & Dispatch Clearance	10 days	17 Oct '24	31 Oct '24	742
744		Receipt At site	7 days	31 Oct '24	11 Nov '24	743

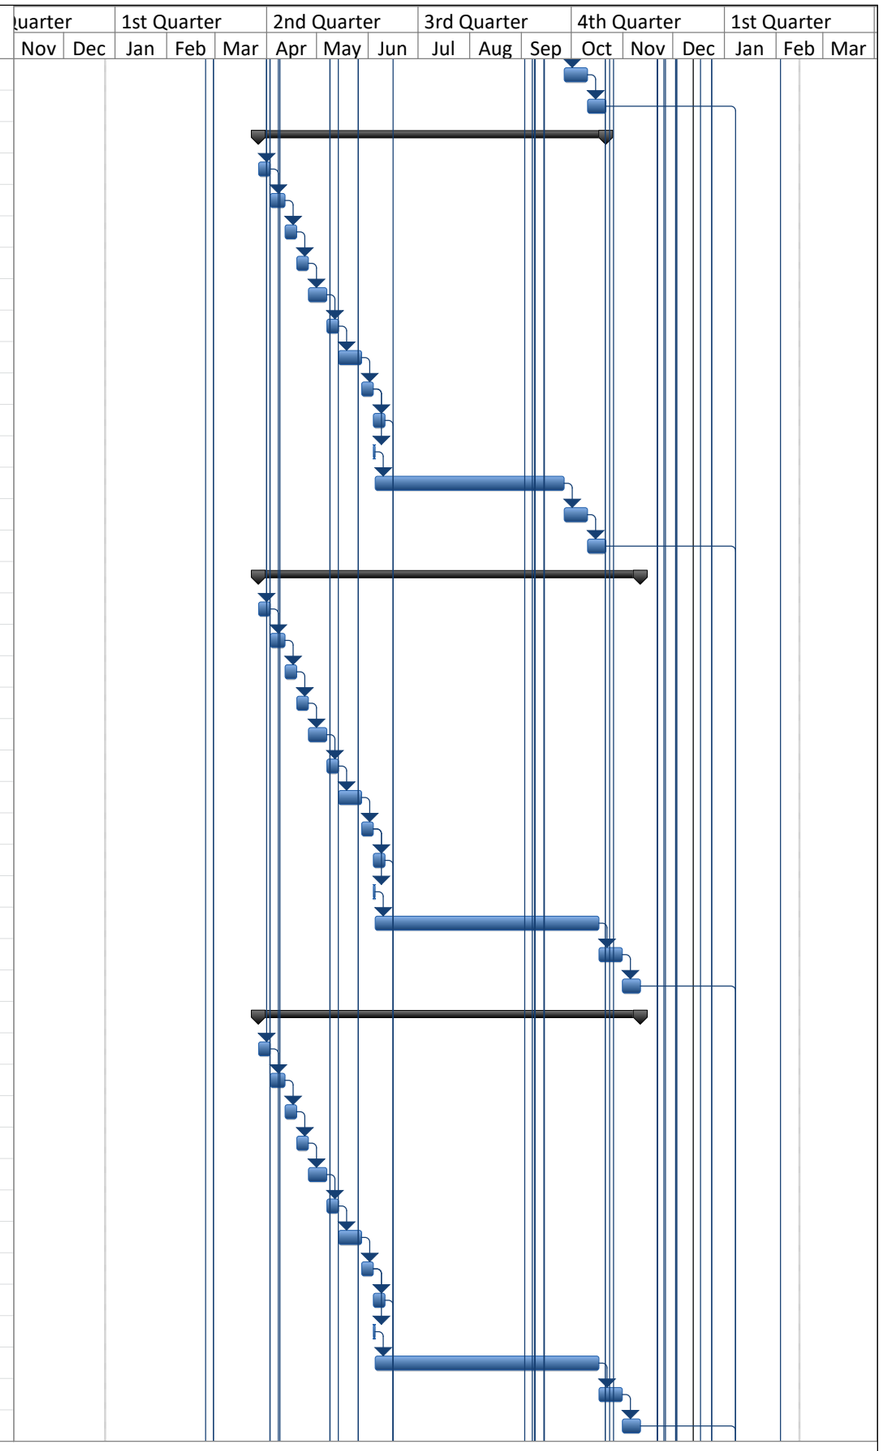

200 m3/hr DM RO Chain at RIL HMD
Start Date: 23.12.26

Task		Project Summary		Inactive Milestone		Manual Summary Rollup		Deadline	
Split		External Tasks		Inactive Summary		Manual Summary		Progress	
Milestone		External Milestone		Manual Task		Start-only			
Summary		Inactive Task		Duration-only		Finish-only			

ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors
745		**Control Valves**	**192.38 days**	**26 Feb '24**	**20 Nov '24**	
746		Submission of Sizing Calculations	7 days	26 Feb '24	05 Mar '24	17,22
747		Receipt of 1st comments	10 days	06 Mar '24	19 Mar '24	746
748		Re-submission	5 days	20 Mar '24	26 Mar '24	747
749		Final Approval	5 days	27 Mar '24	02 Apr '24	748
750		Release of Enquiry	5 days	27 Mar '24	02 Apr '24	748
751		Receipt of Offers	7 days	03 Apr '24	11 Apr '24	750
752		Technical Clearance for Ordering	5 days	12 Apr '24	18 Apr '24	751
753		Ordering	5 days	19 Apr '24	25 Apr '24	752
754		Receipt of Post Order Documents from Vendor	7 days	26 Apr '24	06 May '24	753
755		Submission of Documents	5 days	07 May '24	13 May '24	754
756		Receipt of 1st comments	10 days	14 May '24	27 May '24	755
757		Re-submission	5 days	28 May '24	03 Jun '24	756
758		Final Approval	5 days	04 Jun '24	10 Jun '24	757
759		Manufacturing Clearance	1 day	04 Jun '24	04 Jun '24	757
760		Manufacturing	140 days	04 Jun '24	28 Oct '24	759
761		Inspection & Dispatch Clearance	10 days	28 Oct '24	11 Nov '24	760
762		Receipt At site	7 days	11 Nov '24	20 Nov '24	761
763		**PLC System**	**246 days**	**26 Dec '23**	**03 Dec '24**	
764		Submission of Control Logic	7 days	03 Apr '24	11 Apr '24	17,22,27
765		Receipt of 1st comments	10 days	12 Apr '24	25 Apr '24	764
766		Re-submission	5 days	26 Apr '24	02 May '24	765
767		Final Approval	5 days	03 May '24	09 May '24	766
768		Submission of PLC I/O List	7 days	26 Dec '23	03 Jan '24	
769		Receipt of 1st comments	10 days	04 Jan '24	17 Jan '24	768
770		Re-submission	5 days	18 Jan '24	24 Jan '24	769
771		Final Approval	5 days	25 Jan '24	31 Jan '24	770
772		Release of Enquiry	5 days	12 Apr '24	18 Apr '24	768,764
773		Receipt of Offers	7 days	19 Apr '24	29 Apr '24	772
774		Technical Clearance for Ordering	5 days	30 Apr '24	06 May '24	773
775		Ordering	5 days	07 May '24	13 May '24	774
776		Receipt of Post Order Documents from Vendor	7 days	14 May '24	22 May '24	775
777		Submission of Documents	5 days	23 May '24	29 May '24	776
778		Receipt of 1st comments	10 days	30 May '24	12 Jun '24	777
779		Re-submission	5 days	13 Jun '24	19 Jun '24	778
780		Final Approval	5 days	20 Jun '24	26 Jun '24	779
781		Manufacturing Clearance	1 day	20 Jun '24	20 Jun '24	779
782		Manufacturing	145 days	26 Jun '24	23 Nov '24	780
783		Inspection & Dispatch Clearance	12 days	21 Jun '24	08 Jul '24	781
784		Receipt At site	7 days	25 Nov '24	03 Dec '24	782
785		**Instrument Cables**	**147.88 days**	**05 Mar '24**	**26 Sep '24**	
786		Submission of Cable Schedule	7 days	05 Mar '24	13 Mar '24	614SS
787		Receipt of 1st comments	10 days	14 Mar '24	27 Mar '24	786
788		Re-submission	5 days	28 Mar '24	03 Apr '24	787

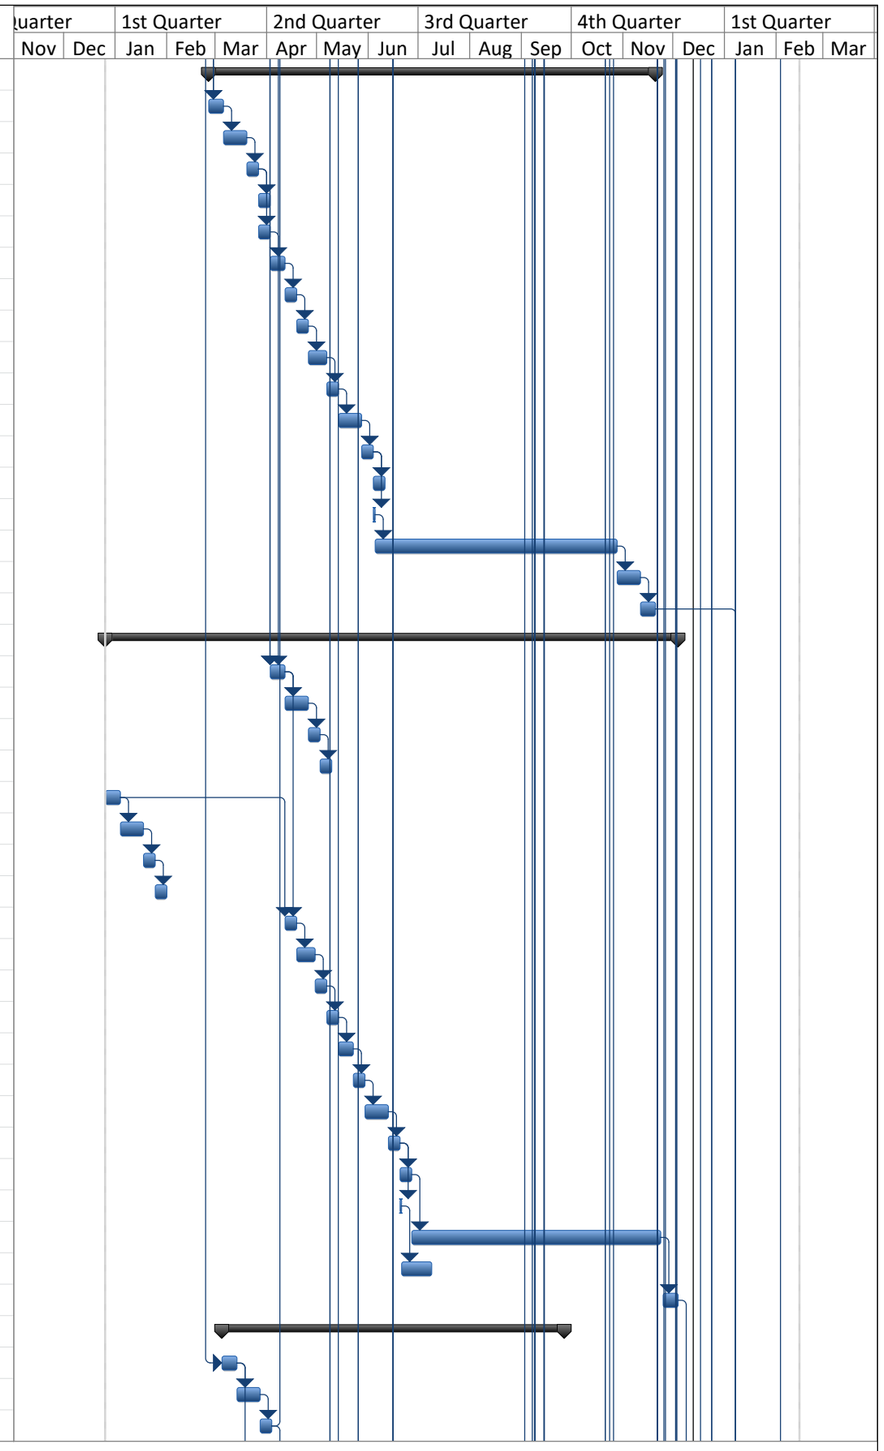

200 m3/hr DM RO Chain at RIL HMD
Start Date: 23.12.26

Task		Project Summary		Inactive Milestone		Manual Summary Rollup		Deadline	
Split		External Tasks		Inactive Summary		Manual Summary		Progress	
Milestone		External Milestone		Manual Task		Start-only			
Summary		Inactive Task		Duration-only		Finish-only			

ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors
789		Final Approval	5 days	04 Apr '24	10 Apr '24	788
790		Release of Enquiry	5 days	14 Mar '24	20 Mar '24	786
791		Receipt of Offers	7 days	21 Mar '24	29 Mar '24	790
792		Technical Clearance for Ordering	5 days	01 Apr '24	05 Apr '24	791
793		Ordering	5 days	08 Apr '24	12 Apr '24	792
794		Receipt of Post Order Documents from Vendor	7 days	15 Apr '24	23 Apr '24	793
795		Submission of Documents	5 days	24 Apr '24	30 Apr '24	794
796		Receipt of 1st comments	10 days	01 May '24	14 May '24	795
797		Re-submission	5 days	15 May '24	21 May '24	796
798		Final Approval	5 days	22 May '24	28 May '24	797
799		Manufacturing Clearance	1 day	22 May '24	22 May '24	797
800		Manufacturing	100 days	22 May '24	03 Sep '24	799
801		Inspection & Dispatch Clearance	10 days	03 Sep '24	17 Sep '24	800
802		Receipt At site	7 days	17 Sep '24	26 Sep '24	801
803		**Junction Box**	**140.88 days**	**09 May '24**	**21 Nov '24**	
804		Release of Enquiry	5 days	09 May '24	15 May '24	688,53,634
805		Receipt of Offers	7 days	16 May '24	24 May '24	804
806		Technical Clearance for Ordering	5 days	27 May '24	31 May '24	805
807		Ordering	5 days	03 Jun '24	07 Jun '24	806
808		Receipt of Post Order Documents from Vendor	7 days	10 Jun '24	18 Jun '24	807
809		Submission of Documents	5 days	19 Jun '24	25 Jun '24	808
810		Receipt of 1st comments	10 days	26 Jun '24	09 Jul '24	809
811		Re-submission	5 days	10 Jul '24	16 Jul '24	810
812		Final Approval	5 days	17 Jul '24	23 Jul '24	811
813		Manufacturing Clearance	1 day	17 Jul '24	17 Jul '24	811
814		Manufacturing	100 days	17 Jul '24	29 Oct '24	813
815		Inspection & Dispatch Clearance	10 days	29 Oct '24	12 Nov '24	814
816		Receipt At site	7 days	12 Nov '24	21 Nov '24	815
817		**SM Box**	**140.88 days**	**09 May '24**	**21 Nov '24**	
818		Release of Enquiry	5 days	09 May '24	15 May '24	804FF
819		Receipt of Offers	7 days	16 May '24	24 May '24	818
820		Technical Clearance for Ordering	5 days	27 May '24	31 May '24	819
821		Ordering	5 days	03 Jun '24	07 Jun '24	820
822		Receipt of Post Order Documents from Vendor	7 days	10 Jun '24	18 Jun '24	821
823		Submission of Documents	5 days	19 Jun '24	25 Jun '24	822
824		Receipt of 1st comments	10 days	26 Jun '24	09 Jul '24	823
825		Re-submission	5 days	10 Jul '24	16 Jul '24	824
826		Final Approval	5 days	17 Jul '24	23 Jul '24	825
827		Manufacturing Clearance	1 day	17 Jul '24	17 Jul '24	825
828		Manufacturing	100 days	17 Jul '24	29 Oct '24	827
829		Inspection & Dispatch Clearance	10 days	29 Oct '24	12 Nov '24	828
830		Receipt At site	7 days	12 Nov '24	21 Nov '24	829
831		**Cable Glands (Instrumentation)**	**76.25 days**	**29 May '24**	**12 Sep '24**	
832		Release of BOM	5 days	29 May '24	04 Jun '24	798

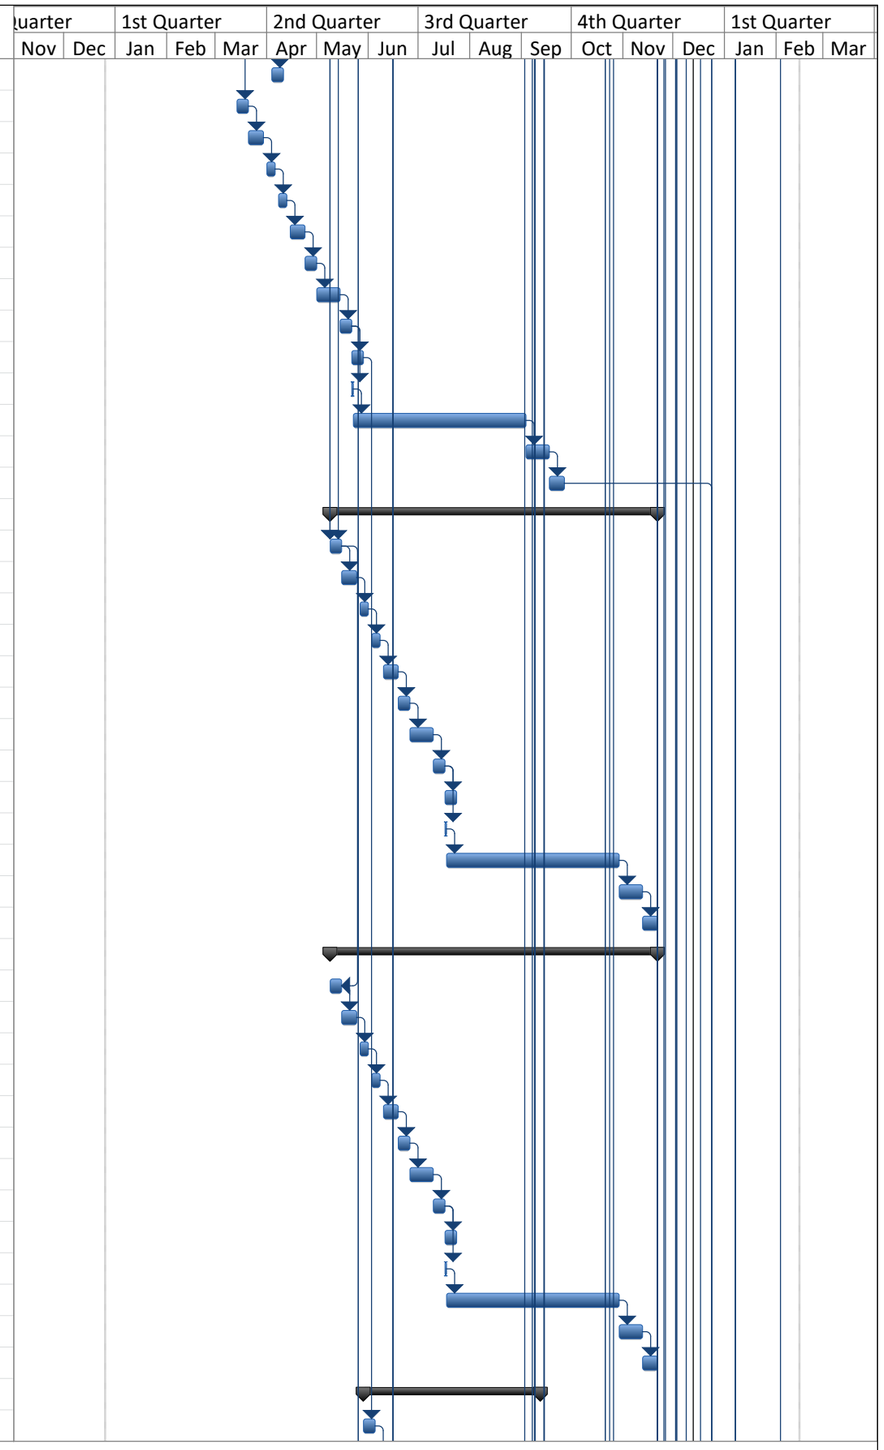

200 m3/hr DM RO Chain at RIL HMD
Start Date: 23.12.26

Task		Project Summary		Inactive Milestone		Manual Summary Rollup		Deadline	
Split		External Tasks		Inactive Summary		Manual Summary		Progress	
Milestone		External Milestone		Manual Task		Start-only			
Summary		Inactive Task		Duration-only		Finish-only			

ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors
833		Receipt of Offers	5 days	05 Jun '24	11 Jun '24	832
834		Ordering & Manufacturing Clearance	5 days	12 Jun '24	18 Jun '24	833
835		Manufacturing	60 days	18 Jun '24	20 Aug '24	834
836		Inspection & Dispatch Clearance	10 days	20 Aug '24	03 Sep '24	835
837		Receipt At site	7 days	03 Sep '24	12 Sep '24	836
838		**Instrument Hook-up Material**	**114.63 days**	**11 Jun '24**	**18 Nov '24**	
839		Submission of Hook-up drawing	7 days	11 Jun '24	19 Jun '24	698,712,726,740
840		Receipt of 1st comments	10 days	20 Jun '24	03 Jul '24	839
841		Re-submission	5 days	04 Jul '24	10 Jul '24	840
842		Final Approval	5 days	11 Jul '24	17 Jul '24	841
843		Release of Enquiry	5 days	11 Jul '24	17 Jul '24	841
844		Receipt of Offers	10 days	18 Jul '24	31 Jul '24	843
845		Ordering & Manufacturing Clearance	5 days	01 Aug '24	07 Aug '24	844
846		Manufacturing	75 days	07 Aug '24	24 Oct '24	845
847		Inspection & Dispatch Clearance	10 days	24 Oct '24	07 Nov '24	846
848		Receipt At site	7 days	07 Nov '24	18 Nov '24	847
849		Completion of Instrumentation Engineering & Procurement	0 days	03 Dec '24	03 Dec '24	684
850		**Civil Construction (By Client)**	**180 days**	**20 May '24**	**22 Nov '24**	
851		Completion of Civil Works	180 days	20 May '24	22 Nov '24	62,71
852		**Erection & Commissioning**	**170.63 days**	**21 Aug '24**	**14 Feb '25**	
853		**Mechanical Erection**	**148.63 days**	**21 Aug '24**	**22 Jan '25**	
854		Mobilization of Thermax Team to Site	7 days	21 Aug '24	29 Aug '24	851SS+90 days
855		Mobilization of Mechanical Contractor's Team to Site	10 days	29 Aug '24	07 Sep '24	854
856		Fabrication & Erection of UF Permeate (Filterate) Storage Tank	45 days	09 Sep '24	24 Oct '24	855
857		Fabrication & Erection of Degassed Water Storage Tank	45 days	25 Oct '24	10 Dec '24	856
858		**Erection of PEB Shed**	**128 days**	**31 Aug '24**	**11 Jan '25**	
859		Inspection of Civil Foundation and taking over for erection	7 days	31 Aug '24	07 Sep '24	851SS+100 days
860		Unloading & Verification of Supplied material	15 days	02 Sep '24	17 Sep '24	133
861		Material shifting to site	7 days	18 Sep '24	25 Sep '24	860
862		Structural Erection	70 days	25 Sep '24	06 Dec '24	861
863		Roof Sheeting work	35 days	06 Dec '24	11 Jan '25	862
864		Cladding, Fixing of Turboventilator	35 days	06 Dec '24	11 Jan '25	862
865		**Erection of Equipment**	**141.88 days**	**28 Aug '24**	**22 Jan '25**	
866		Erection of Auto Backwash Filters	5 days	09 Sep '24	13 Sep '24	219,855
867		Erection of Basket Filters	2 days	09 Sep '24	10 Sep '24	233,855
868		Erection of UF Modules	20 days	09 Sep '24	28 Sep '24	247,855
869		Erection of Micron Cartridge Filters	4 days	09 Sep '24	12 Sep '24	261,855
870		Erection of Degasser Tower	5 days	09 Sep '24	13 Sep '24	187,855
871		Erection of RO Skids	7 days	09 Sep '24	16 Sep '24	196,855
872		Erection of MB Vessels	3 days	09 Sep '24	11 Sep '24	178,855
873		Erection of Non-Metallic Tanks	5 days	28 Aug '24	03 Sep '24	387
874		Erection of Pumps	25 days	21 Oct '24	15 Nov '24	289,303,317,855

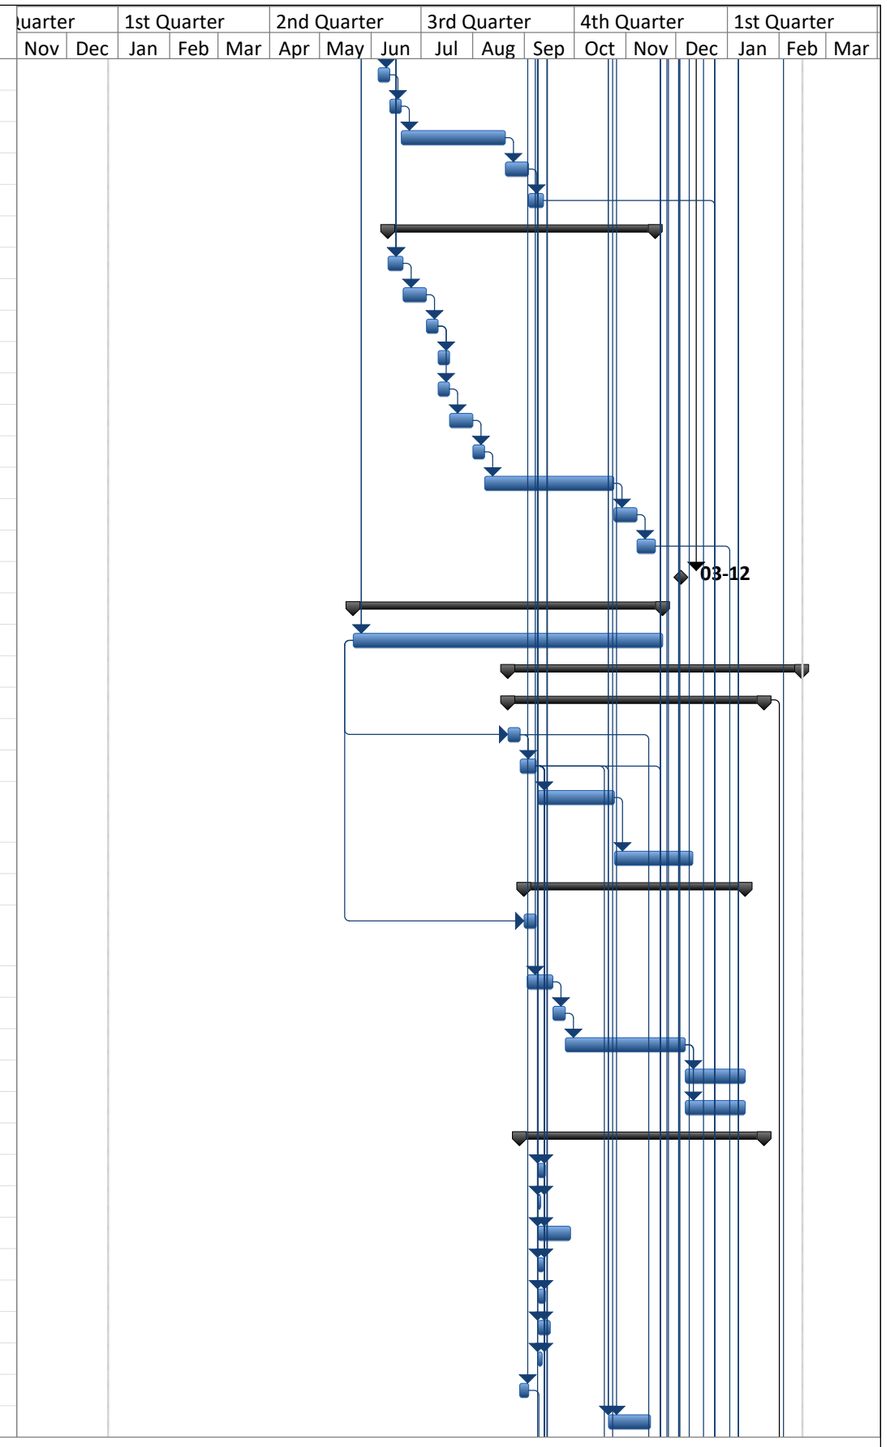

200 m3/hr DM RO Chain at RIL HMD
Start Date: 23.12.26

Task		Project Summary		Inactive Milestone		Manual Summary Rollup		Deadline	
Split		External Tasks		Inactive Summary		Manual Summary		Progress	
Milestone		External Milestone		Manual Task		Start-only			
Summary		Inactive Task		Duration-only		Finish-only			

ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors
875		Erection of Blowers	10 days	09 Sep '24	19 Sep '24	331,345,855
876		Erection of Agitators	10 days	09 Sep '24	19 Sep '24	373,873,855
877		Erection of Dosing Pumps	10 days	09 Sep '24	19 Sep '24	359,855
878		Erection of Pipe Supports	30 days	18 Oct '24	19 Nov '24	537,855
879		Erections of Piping With Valves	60 days	21 Nov '24	22 Jan '25	406,420,434,448,462,476,4
880		Erections of Air Grid	8 days	09 Sep '24	17 Sep '24	551,855
881		**E & I Erection**	**66.63 days**	**14 Nov '24**	**22 Jan '25**	
882		E & I Contractor Mobilization	10 days	14 Nov '24	25 Nov '24	854FS+75 days
883		Fabrication and Erection of Support for cable tray, LPBS, Junction Box etc.	30 days	27 Nov '24	28 Dec '24	657,882
884		Erection of PLC Panel	4 days	03 Dec '24	07 Dec '24	784,882
885		Erection of VFD Panel	4 days	27 Nov '24	02 Dec '24	598,882
886		Earthing work	30 days	25 Nov '24	26 Dec '24	583,882
887		Installation of Cable tray	20 days	03 Dec '24	24 Dec '24	648,882,883SS+5 days
888		Electrical Cable laying	10 days	24 Dec '24	02 Jan '25	630,887
889		Instrumentation Cable laying	7 days	24 Dec '24	31 Dec '24	802,887
890		Glanding and Termination of Electrical cable	15 days	24 Dec '24	08 Jan '25	664,888SS
891		Glanding and Termination of Instrument cable	7 days	24 Dec '24	31 Dec '24	837,889SS
892		Erection of field instrument	10 days	07 Jan '25	17 Jan '25	702,716,730,744,762,879FS
893		Erection of Plant lighting	25 days	12 Dec '24	07 Jan '25	682
894		Impulse tubing	20 days	02 Jan '25	22 Jan '25	848,892FS-15 days
895		RFSU	0 days	22 Jan '25	22 Jan '25	853,881
896		**Precommissioning & Commissioning**	**22 days**	**23 Jan '25**	**14 Feb '25**	
897		MCC Charging (by Client)	4 days	23 Jan '25	27 Jan '25	895
898		No Load Trial of Equipment	7 days	23 Jan '25	30 Jan '25	895
899		Flushing	7 days	30 Jan '25	06 Feb '25	898
900		Load Trial of Equipment	8 days	01 Feb '25	10 Feb '25	899FS-5 days
901		PLC Loop Checking	4 days	23 Jan '25	27 Jan '25	895
902		Membrane Loading	7 days	03 Feb '25	10 Feb '25	275,899FS-3 days
903		Resin Charging	4 days	06 Feb '25	10 Feb '25	899
904		Commissioning	7 days	07 Feb '25	14 Feb '25	902FS-3 days

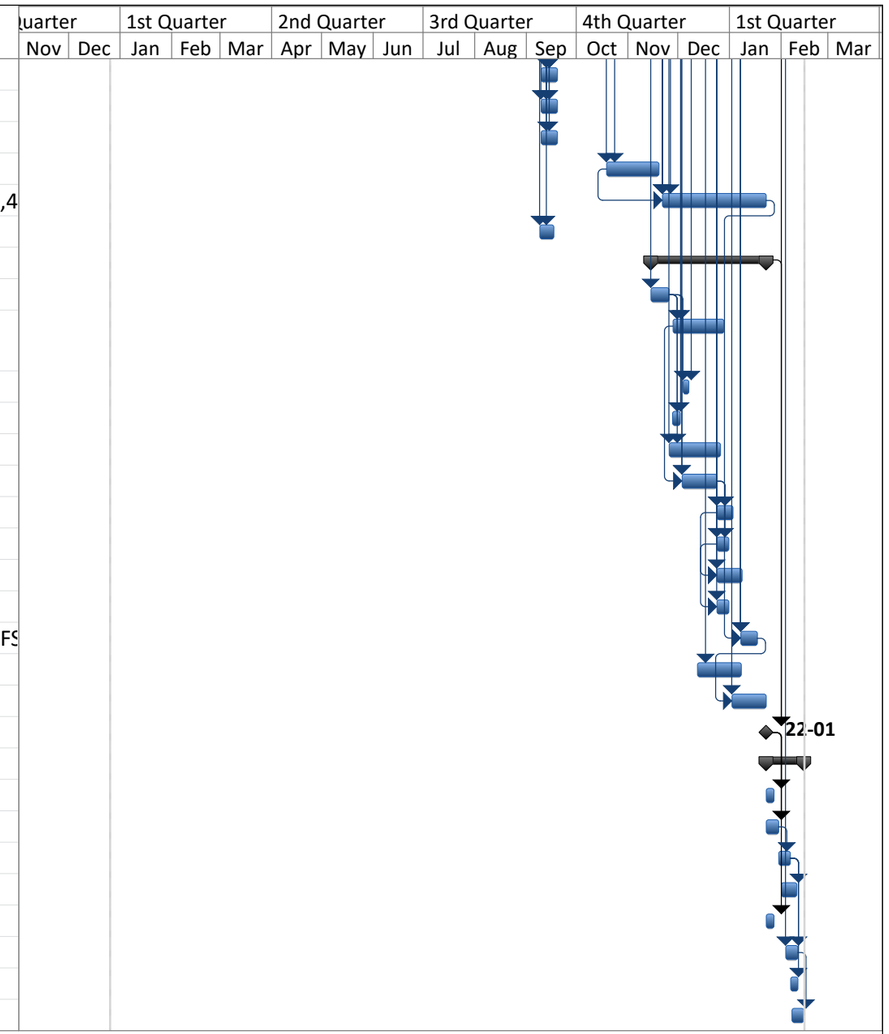

200 m3/hr DM RO Chain at RIL HMD
Start Date: 23.12.26

Task		Project Summary		Inactive Milestone		Manual Summary Rollup		Deadline	
Split		External Tasks		Inactive Summary		Manual Summary		Progress	
Milestone		External Milestone		Manual Task		Start-only			
Summary		Inactive Task		Duration-only		Finish-only			
